



Arkansas State Highway Commission Meeting

December 4, 2024



Associated General Contractors of Arkansas **SKILL, INTEGRITY, RESPONSIBILITY (SIR) AWARD**

01

**Minutes of the October 2, 2024
Meeting**

02

Consideration of Minute Orders

03

Updates

State Highway Financial Report

Patrick Patton, CPA


Chief Fiscal Officer

SFY 2025 BUDGETED VS. ACTUAL EXPENSES – By Budget Category

■ BUDGETED ■ ACTUAL
(MILLIONS)

October

VARIANCE	\$0.0	\$0.7	-\$0.2	-\$1.7	-\$3.6	-\$7.7	-\$12.6
% CHANGE	0.0%	17.5%	-16.7%	-4.7%	-32.4%	-51.0%	-18.7%

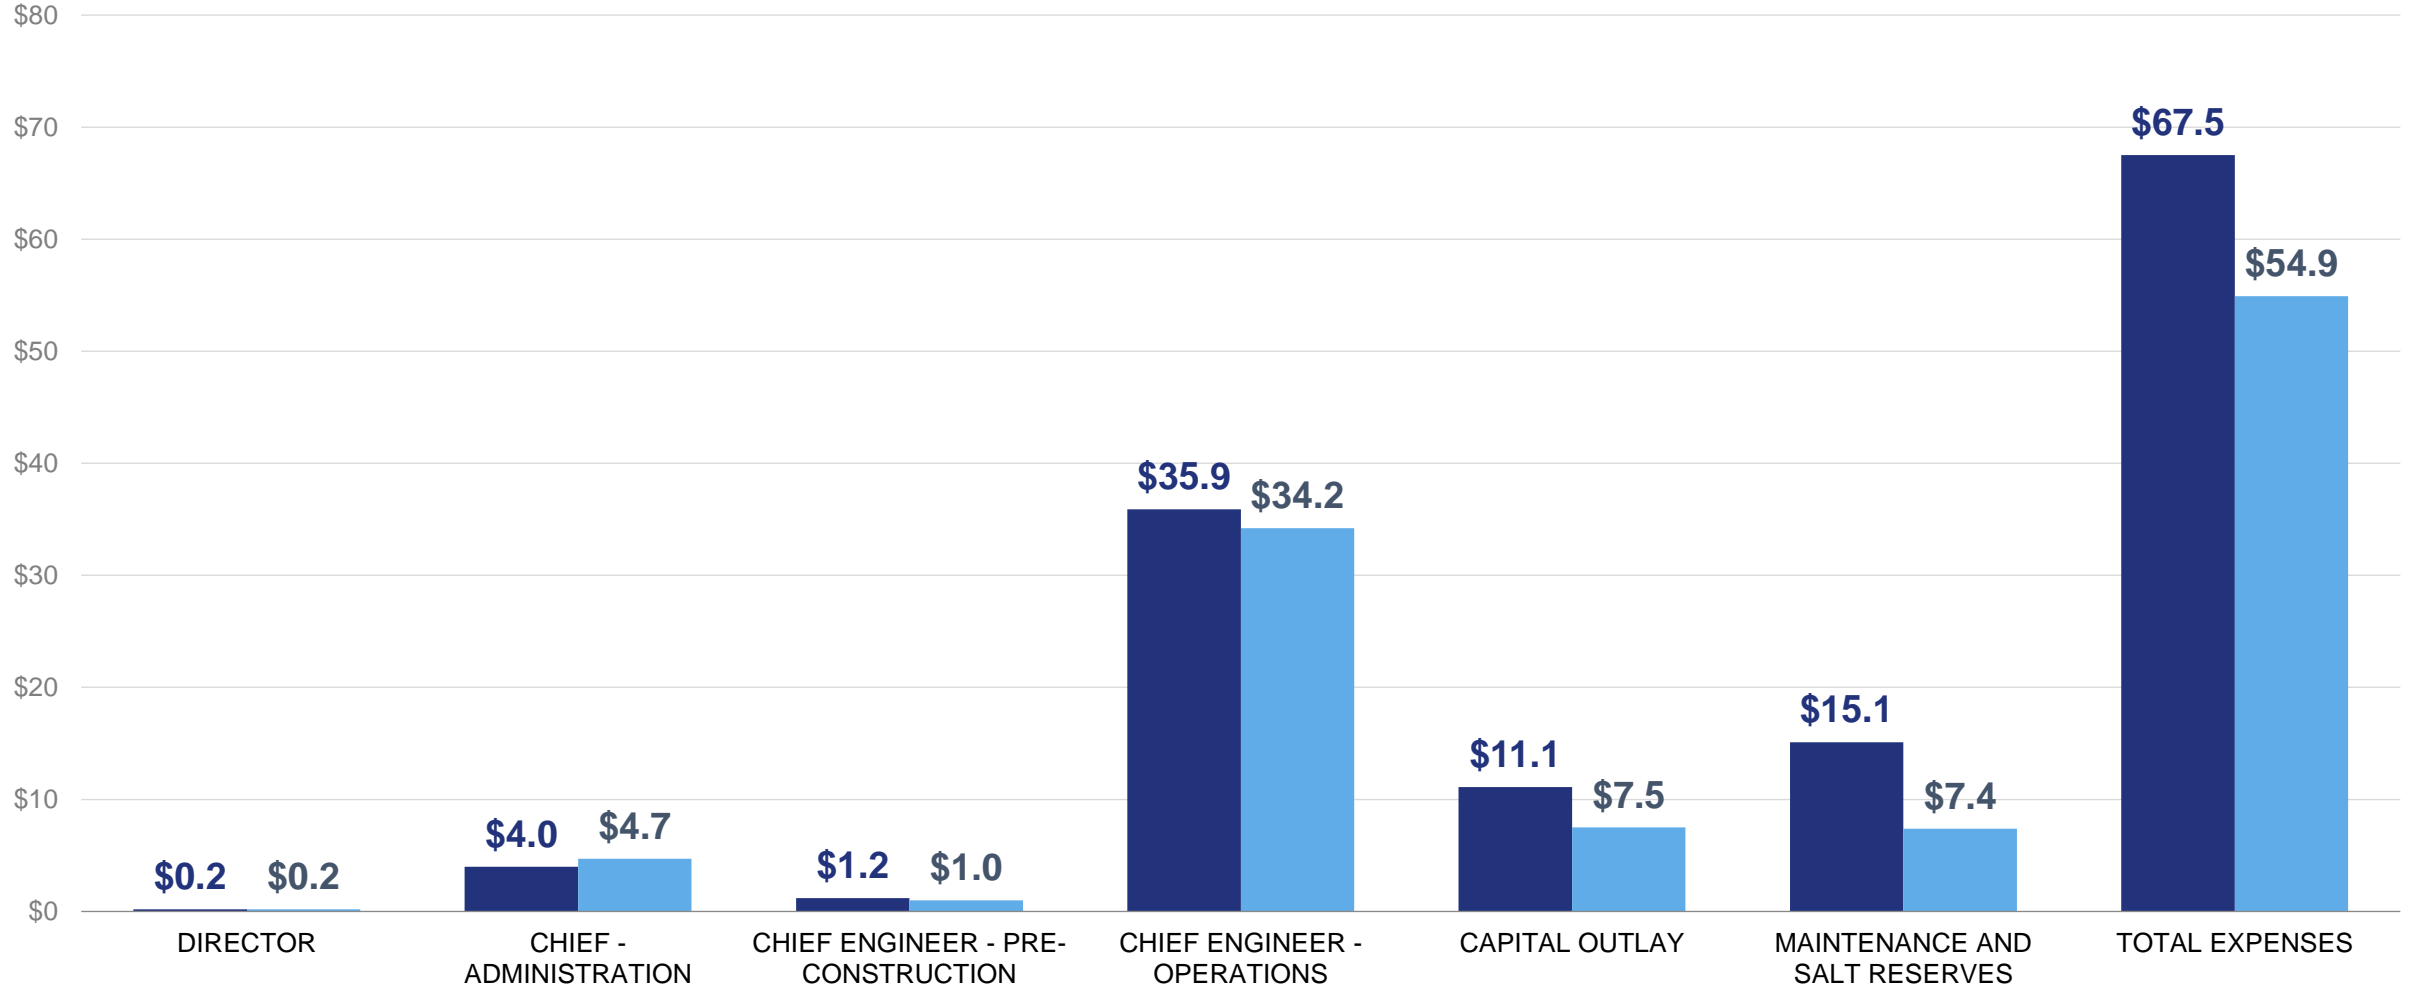


SFY 2025 BUDGETED VS. ACTUAL EXPENSES – By Operational Category

October

■ BUDGETED ■ ACTUAL
(MILLIONS)

VARIANCE	-\$12.6	-\$0.4	\$0.6	-\$0.2	-\$12.6
% CHANGE	-21.9%	-10.0%	18.2%	-7.4%	-18.7%

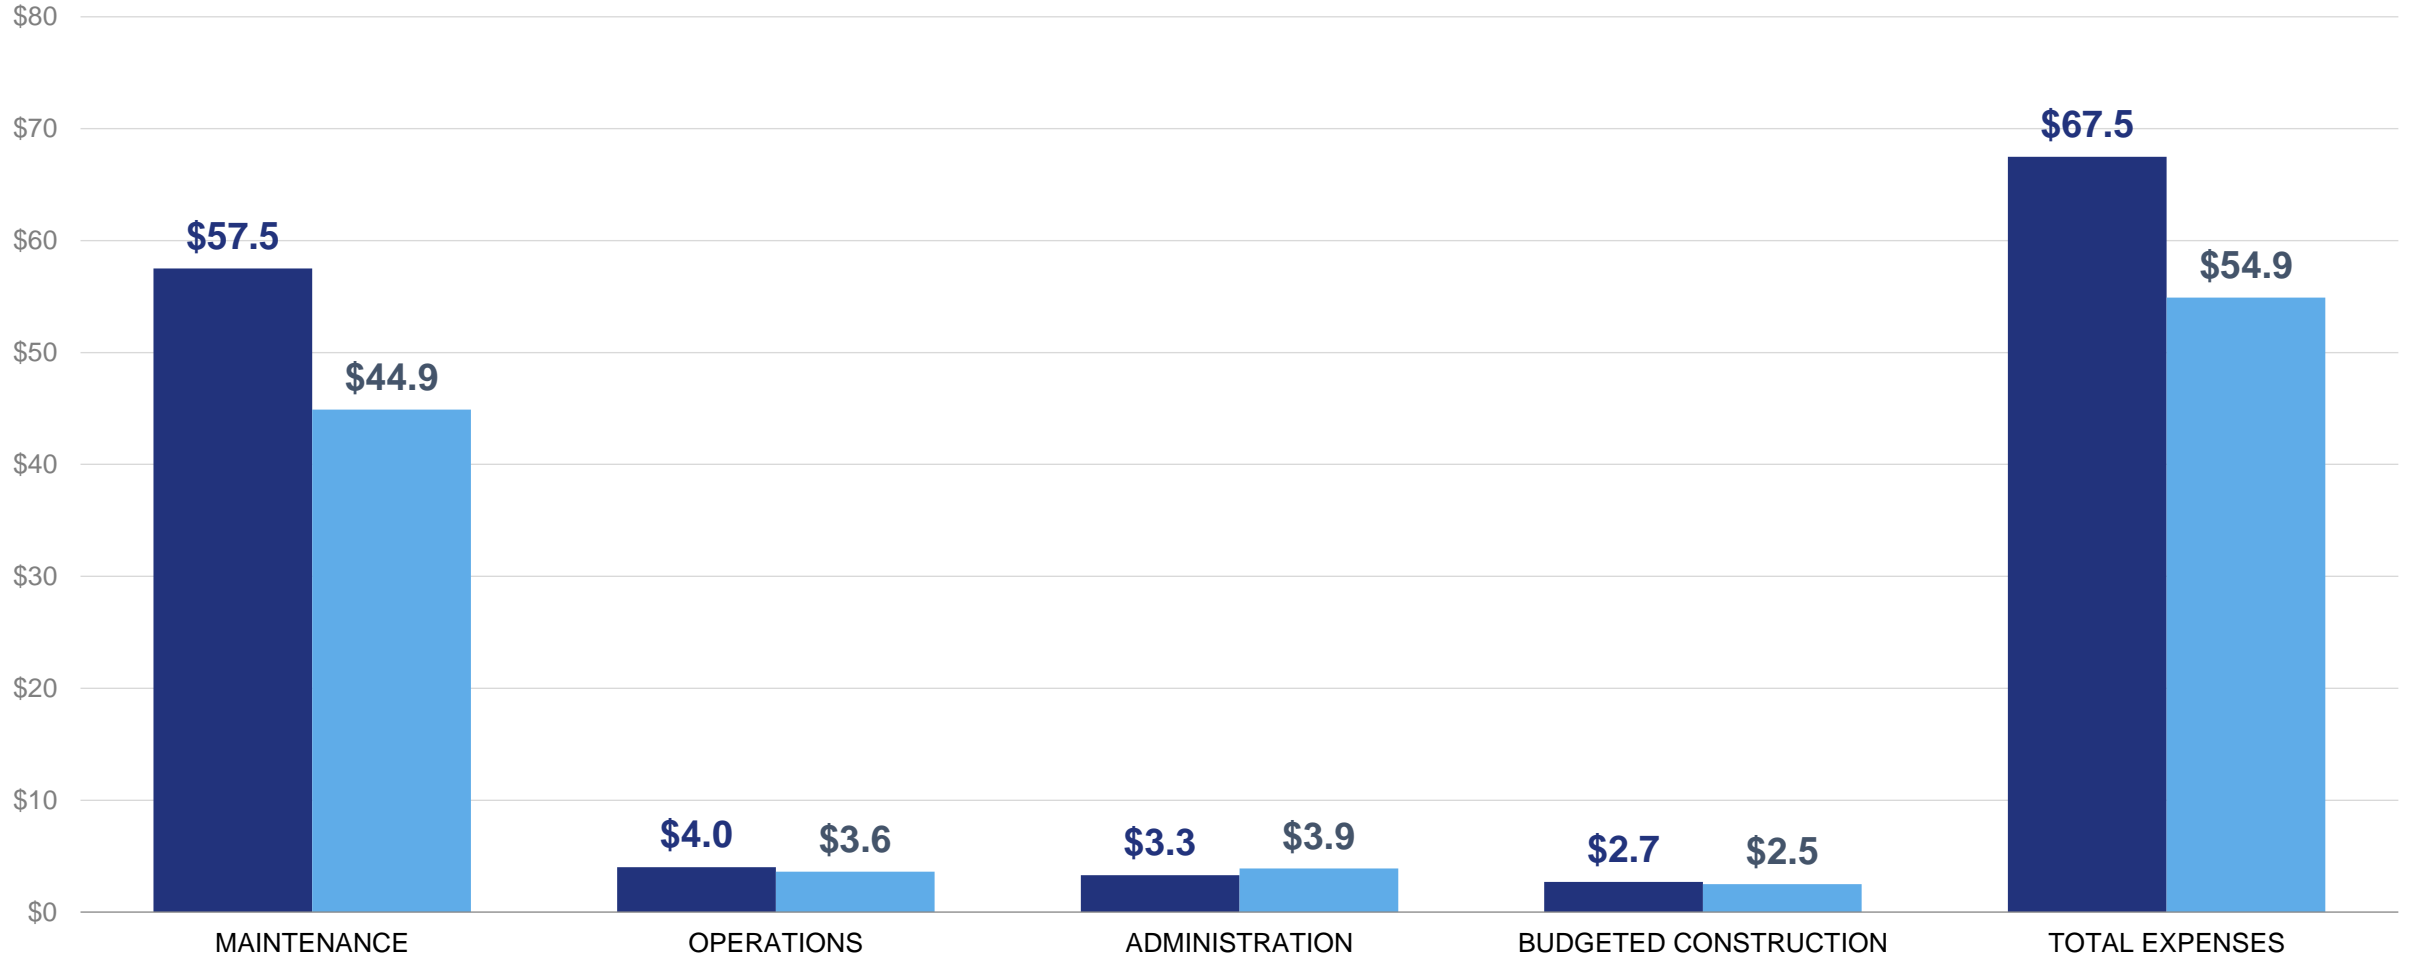


SFY 2024 vs. SFY 2025 ACTUAL REVENUE

October

■ FY 2024 ■ FY 2025
(MILLIONS)

VARIANCE	-\$11.2	\$3.2	-\$1.6	\$0.5	\$0.2	-\$1.2	\$0.6	-\$9.5
% CHANGE	-10.5%	3.5%	-4.6%	8.5%	10.0%	-38.7%	28.6%	-3.9%

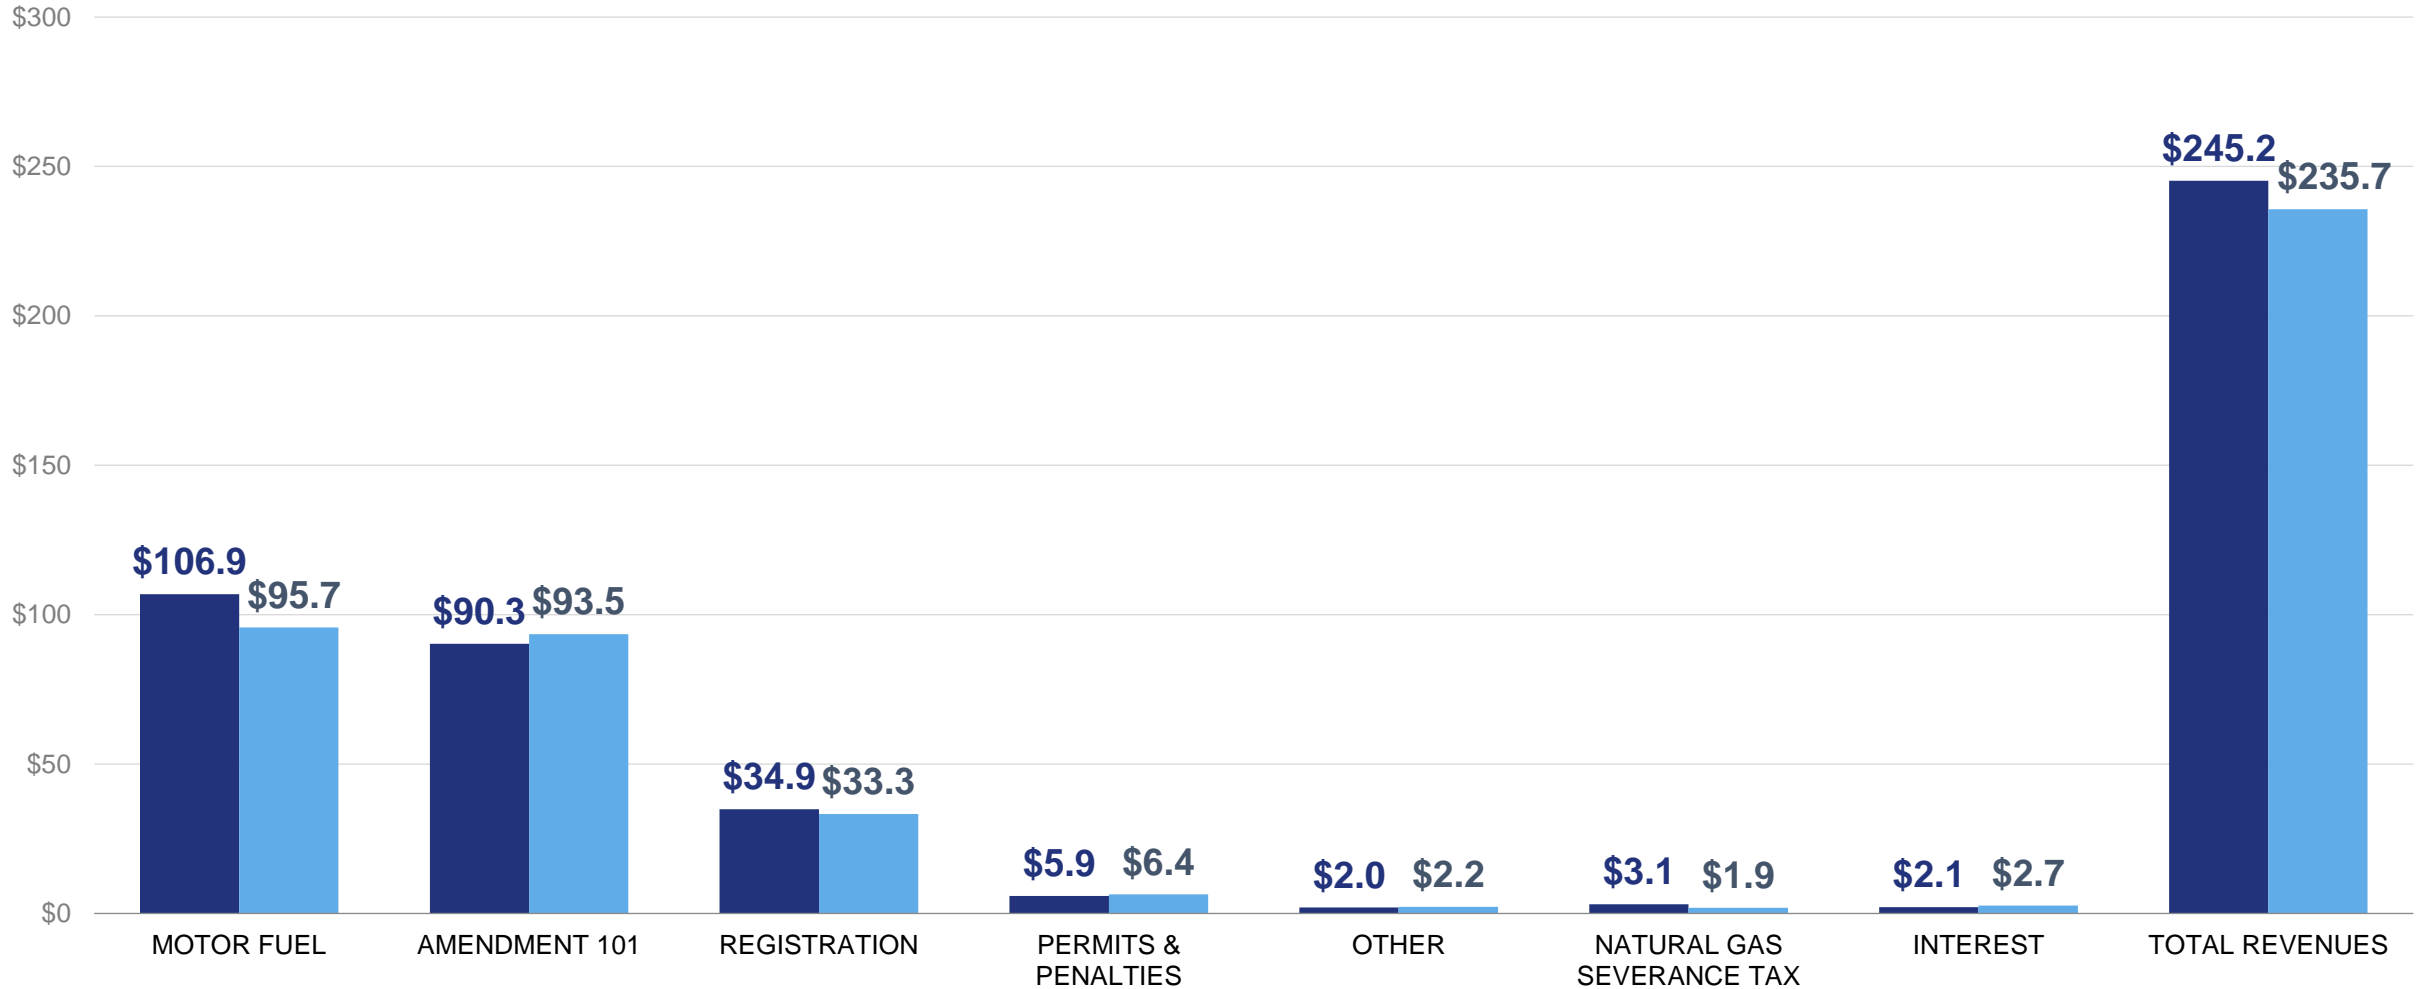


SFY 2025 BUDGETED VS. ACTUAL REVENUE

October

■ BUDGETED ■ ACTUAL

(MILLIONS)

VARIANCE	-\$11.4	\$3.4	-\$1.6	\$0.5	\$0.2	\$0.0	\$0.6	-\$8.3
% CHANGE	-10.6%	3.8%	-4.6%	8.5%	10.0%	0.0%	28.6%	-3.4%

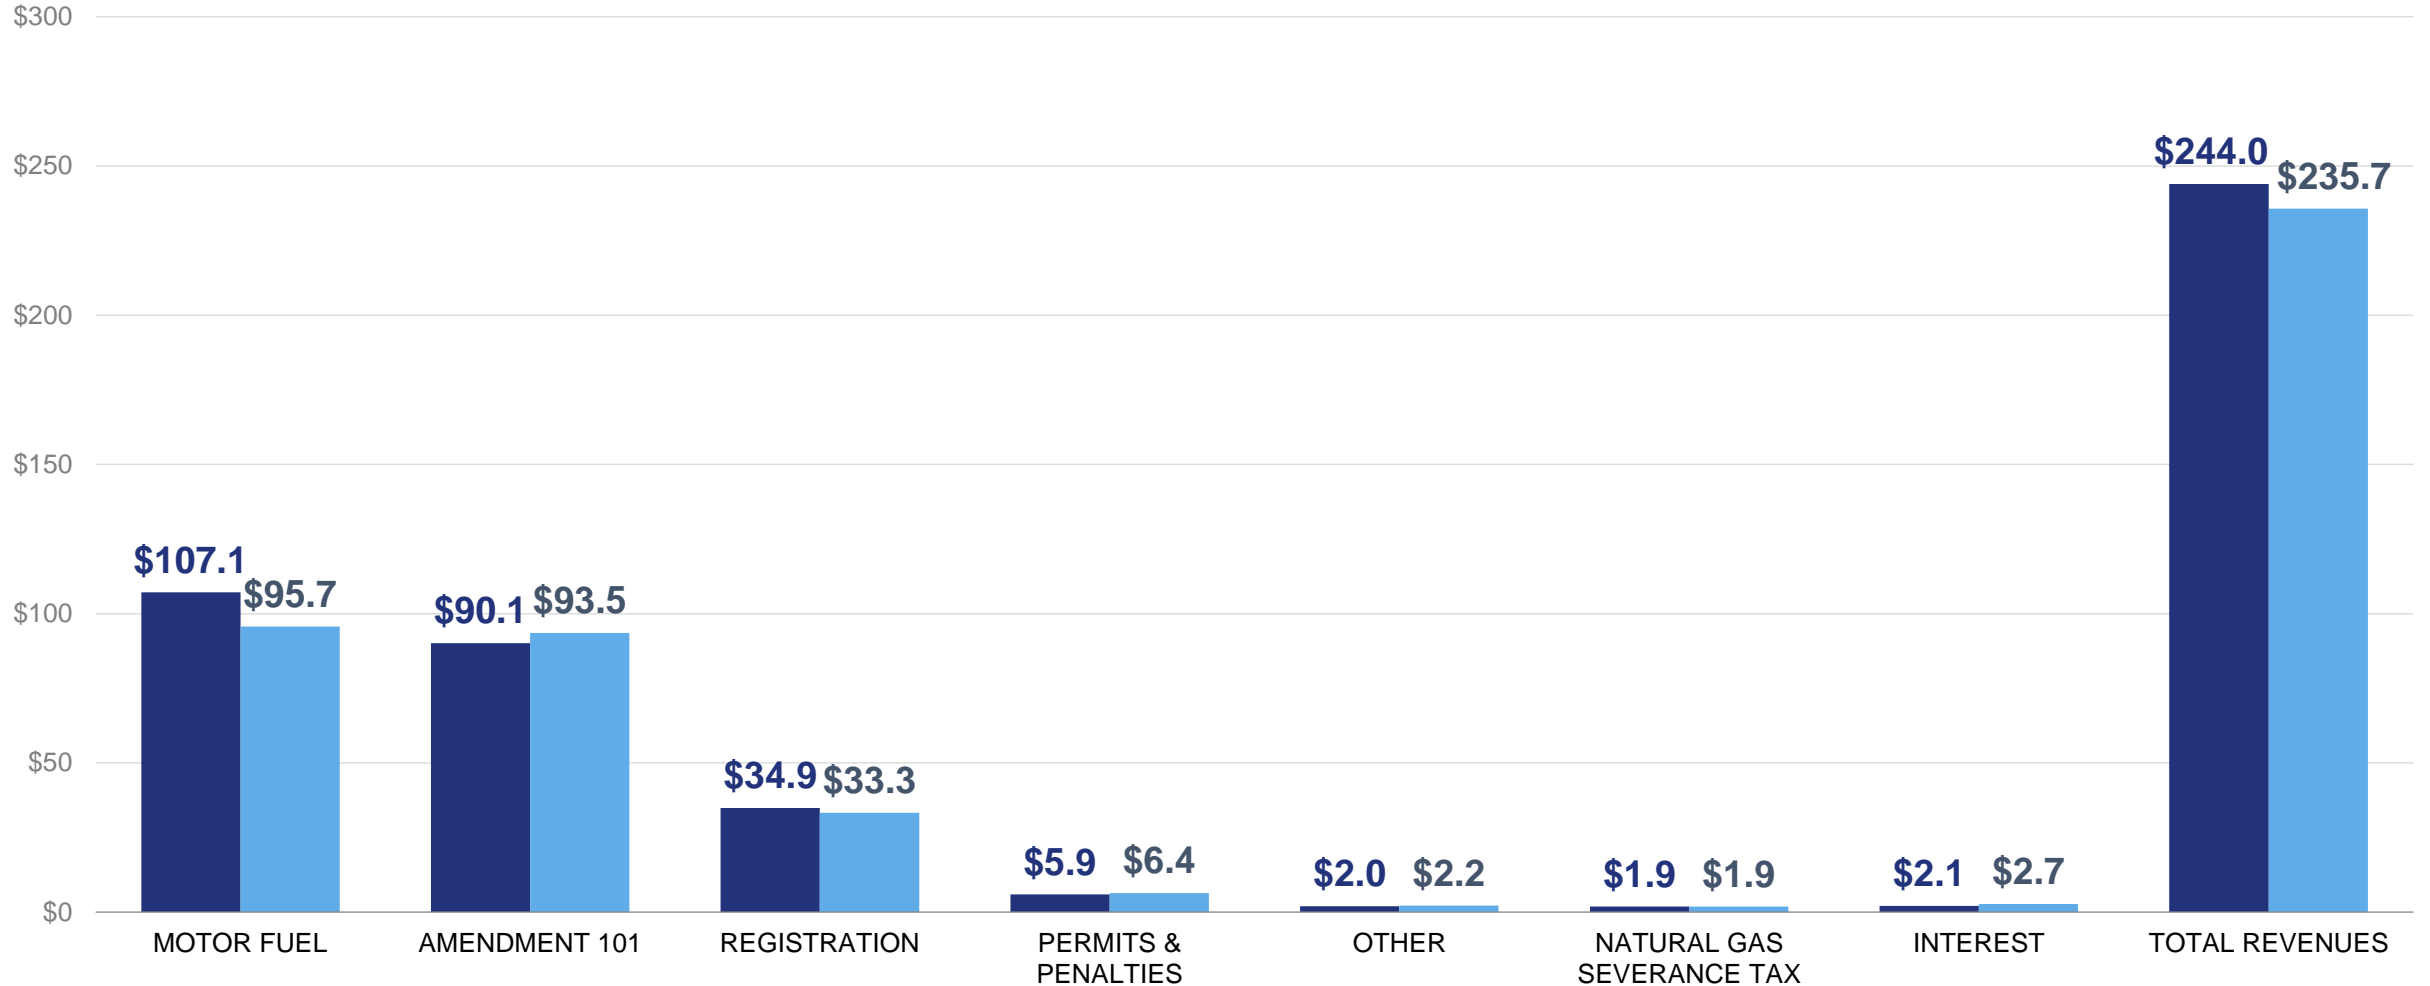

SFY 2024 vs. SFY 2025 ACT 416 ACTUAL REVENUE

■ FY 2024 ■ FY 2025

October

(MILLIONS)



SFY 2025 BUDGETED vs. ACT 416 ACTUAL REVENUE

October

■ BUDGET ■ ACTUAL
(MILLIONS)



SFY 2024 vs. SFY 2025 FUEL CONSUMPTION

October

■ FY 2024 ■ FY 2025
(MILLION GALLONS)


VARIANCE
% CHANGE

-8.4
-1.6%

6.0
2.5%

0.00
0.0%

-2.4
-0.3%

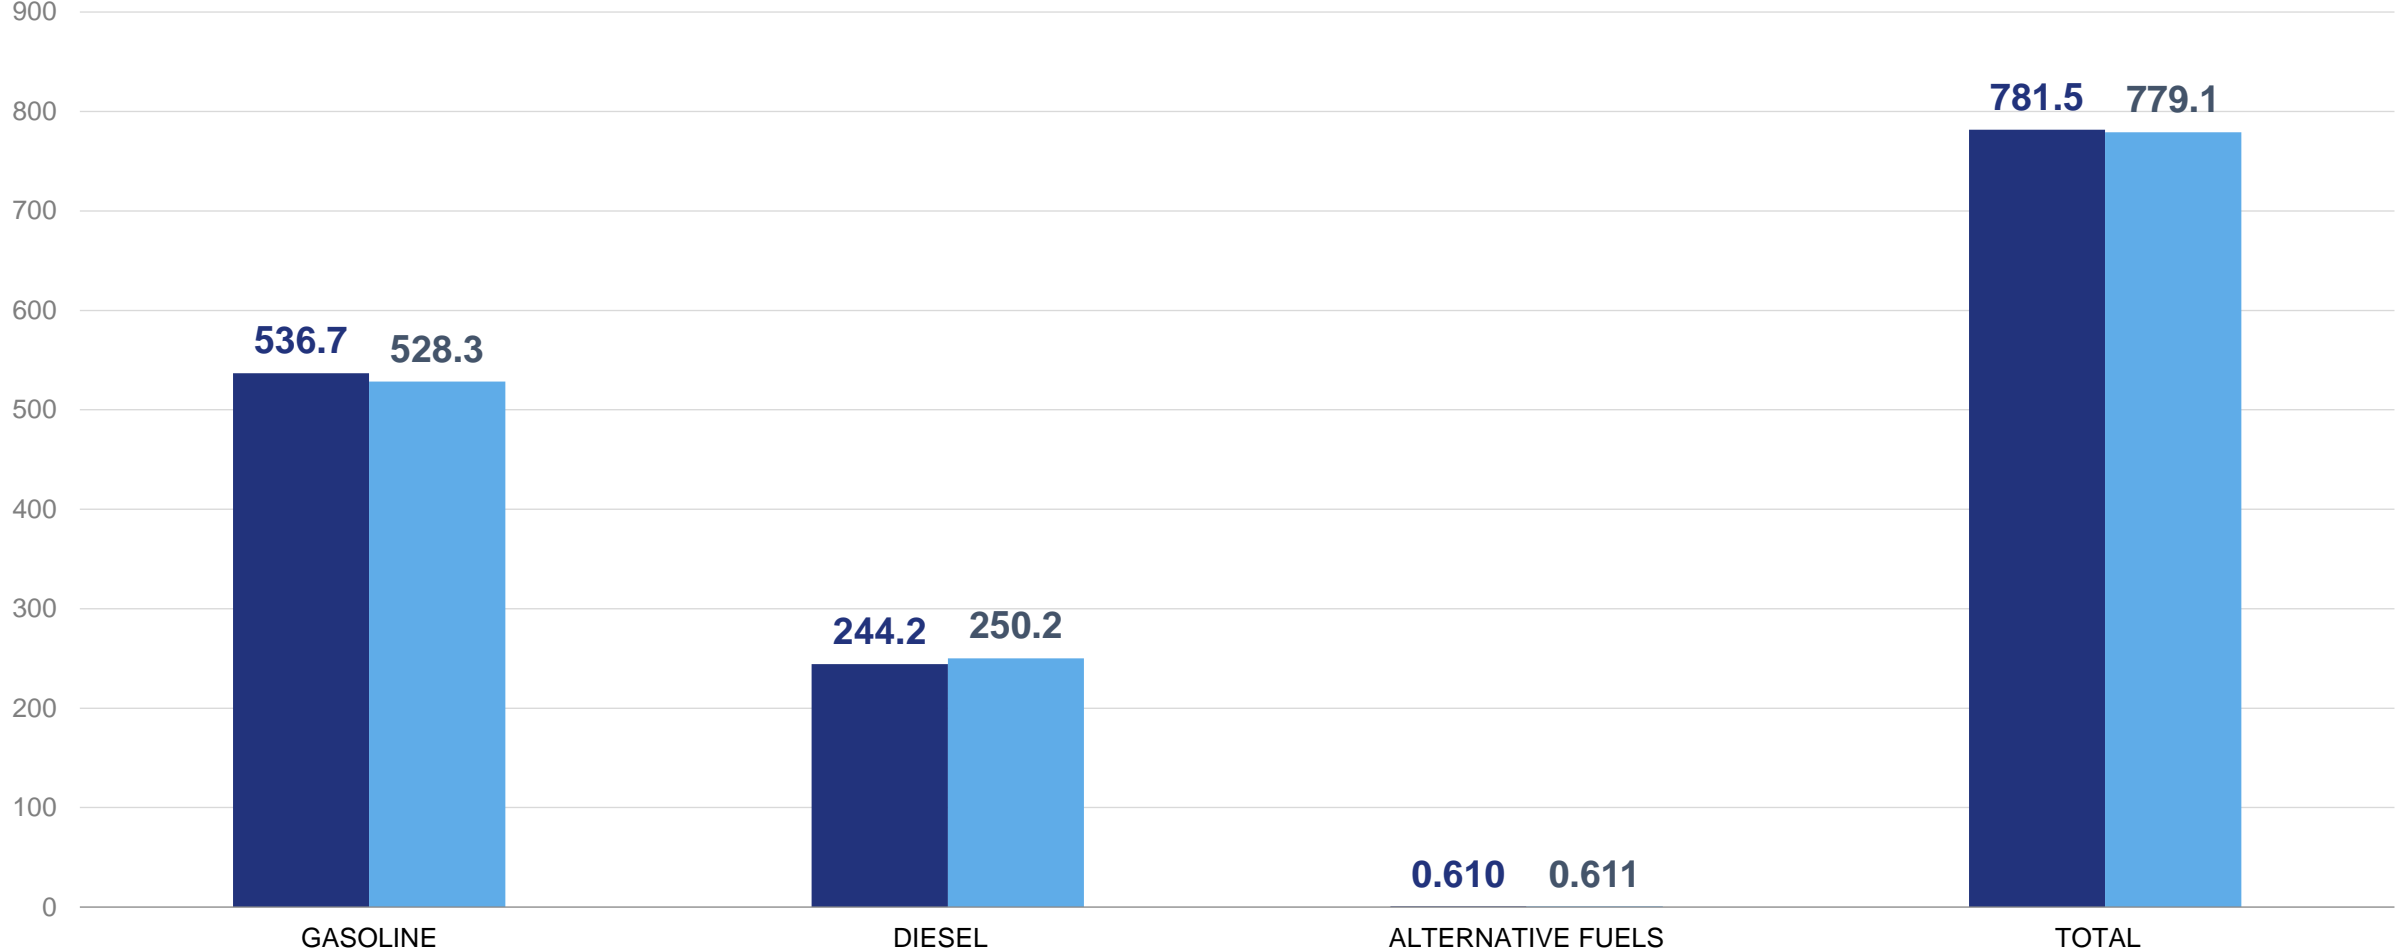



Arkansas Fuel Consumption

ROLLING 12-MONTH COMPARISON

	Previous 12 Months (gallons)	Current 12 Months (gallons)	Variance
Gasoline	1,539,818,562	1,548,075,098	0.54%
Diesel	735,996,376	749,936,420	1.89%
Alternative	1,631,359	1,870,491	14.66%
Total	2,277,446,297	2,299,882,009	0.99%

Federal and State Legislative Activities

Kevin Thornton, P.E.

Chief – Administration

2025 Federal Funding


We are Operating Under a Continuing Resolution

The Continuing Resolution expires December 20th





Arkansas US House Delegation

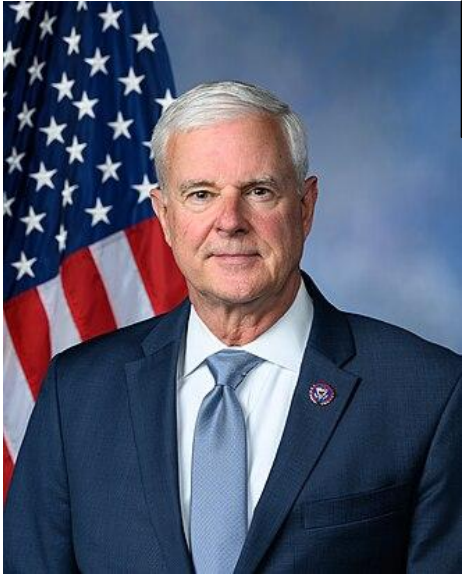

Congressman
Steve Womack

Member of House
Appropriations Committee

Chair of Transportation,
Housing and Urban
Development Subcommittee



Congressman
Rick Crawford


Member of House
Transportation and
Infrastructure Committee

Chair of Highways and Transit
Subcommittee



Congressman
Bruce Westerman


Member of House
Transportation and
Infrastructure Committee



Congressman
French Hill

Vice-Chairman of the House
Financial Services Committee

Chairman Digital Assets,
Financial Technology and
Inclusion Subcommittee

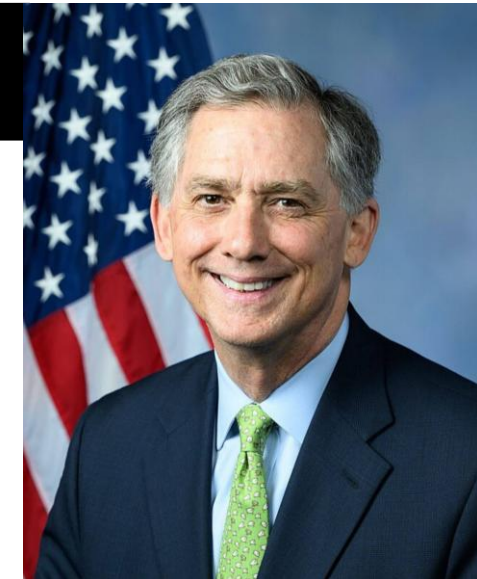




Helena Bridge Rehabilitation

GRANT AWARD

- Total Project Cost: \$57 Million
- Grant Award Amount: \$44 Million
- ARDOT and MDOT will split project costs 50/50



2025 REGULAR SESSION IMPORTANT DATES

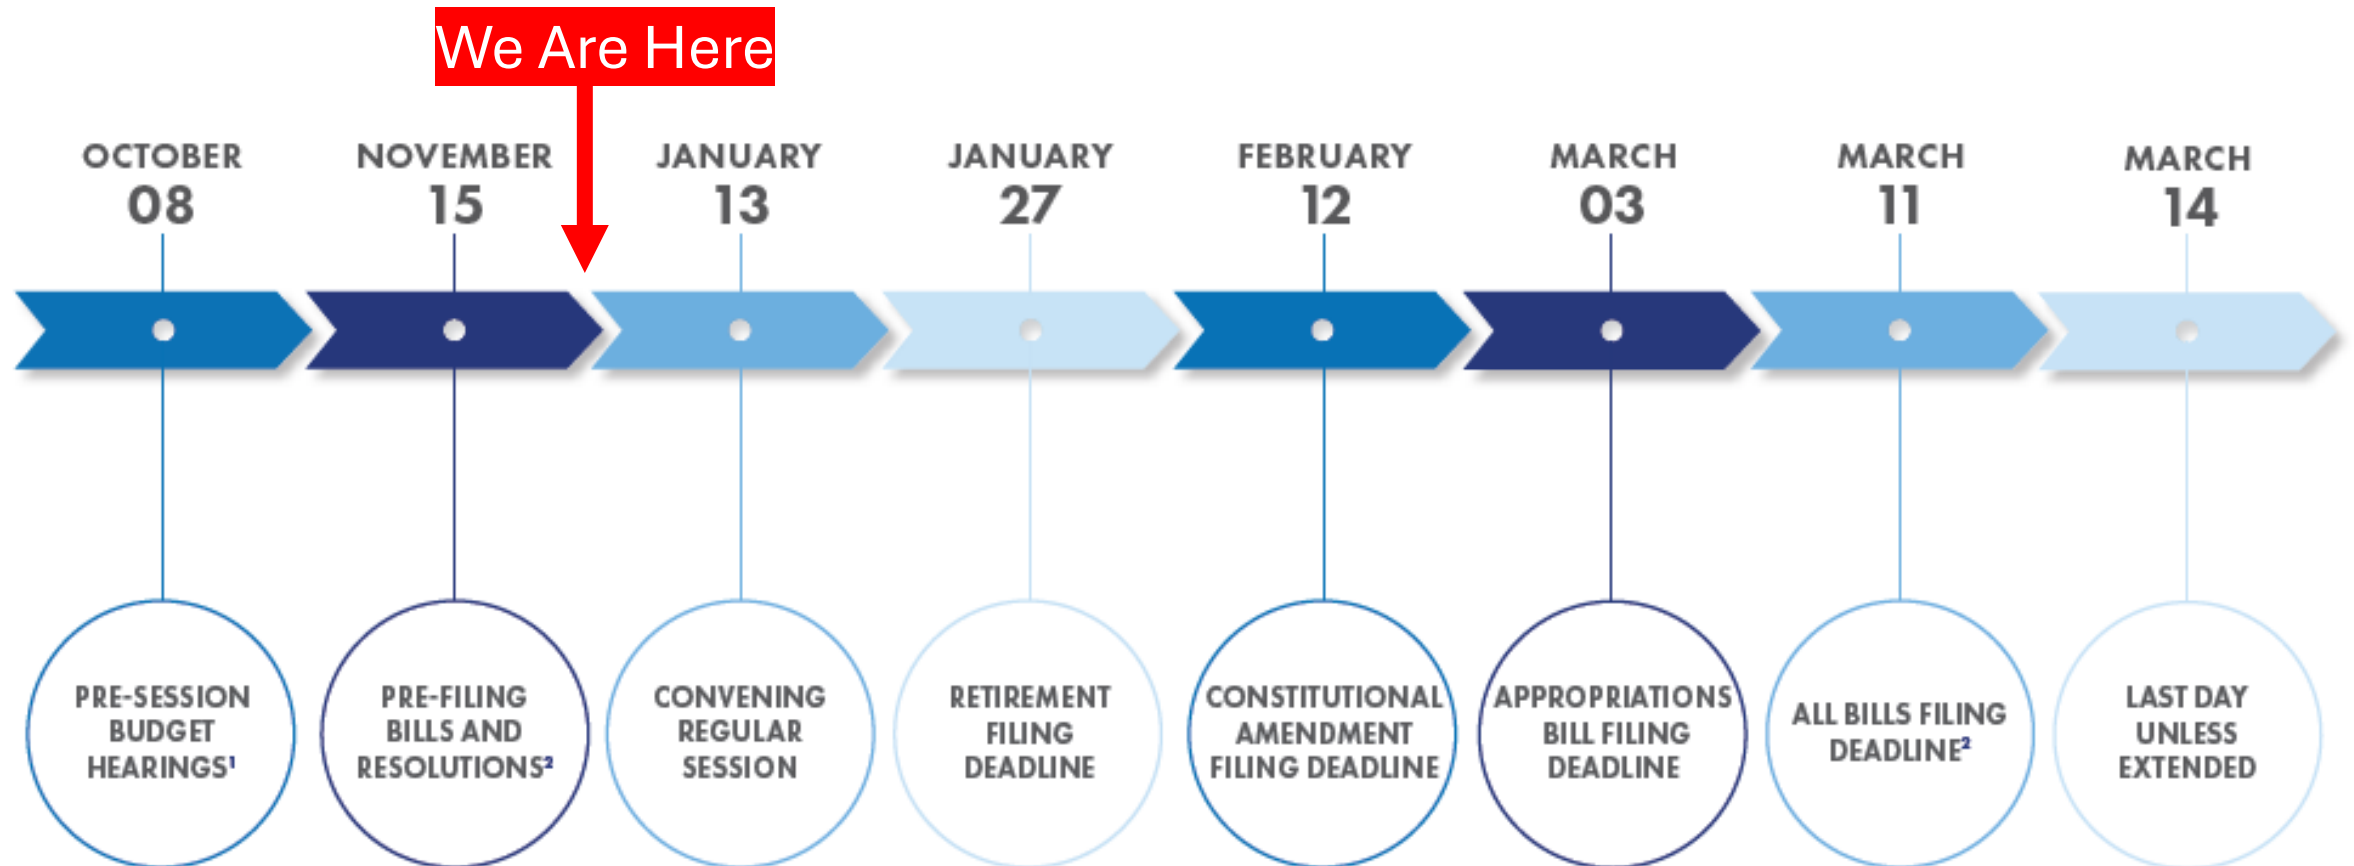

¹OCTOBER 24 - ARDOT BUDGET HEARING

²NO BILL MAY BE FILED THE LAST THREE DAYS OF A SESSION

95th Arkansas General Assembly



SENATE

35 Total Members

1 New Member

HOUSE

100 Total Members

13 New Members

Outgoing Member - Senate



**Linda
Chesterfield**

Incoming Member - Senate



**Jamie
Scott**

Senate - Transportation, Technology & Legislative Affairs Committee



Chair
**Ricky
Hill**



Vice Chair
**Jonathon
Dismang**



**Mark
Johnson**



**Matt
Stone**



**Tyler
Dees**



**Fred
Love**



**Jamie
Scott**



**Joshua
Bryant**

Outgoing Members - House



**Mark
Berry**



**Charlene
Fite**



**Lanny
Fite**



**Deborah
Ferguson**



**Jack
Fortner**



**Vivian
Flowers**



**Delia
Haak**



**DeAnna
Hodges**



**Grant
Hodges**



**Josh
Miller**



**Milton
Nicks**



**Jamie
Scott**



**Danny
Watson**

Incoming Members - House



**Jason
Nazarenko**



**Diana
Gonzales
Worthen**



**Nicholas
Burkes**



**Randy
Torres**



**Brad
Hall**



**James
Eaton**



**Jessie
McGruder**



**Alyssa
Brown**



**Lincoln
Barnett**



**Glenn
Barnes**



**Tracy
Steele**




**Paul
Childress**




**Dolly
Henley**

House – Public Transportation Committee



(TBD)
Chair



(TBD)
Vice-Chair



Stan
Berry



Harlan
Breaux



Alyssa
Brown



Nicholas
Burkes



Joey L.
Carr



Paul
Childress



Matt
Duffield



Brad
Hall



RJ
Hawk



Mike
Holcomb



Mark D.
McElroy



Jon
Milligan



Chad
Puryear



Marcus E.
Richmond



Tara
Shephard



Tracy
Steele



Trey
Steimel



Randy
Torres



David
Whitaker




Richard
Womack

Efficiency Review Recommendation Implementation

Crystal Woods

Assistant Chief – Administration

Arkansas Department of Transportation
Arkansas Legislative Council
Efficiency Study Recommendations
Rules for Implementation

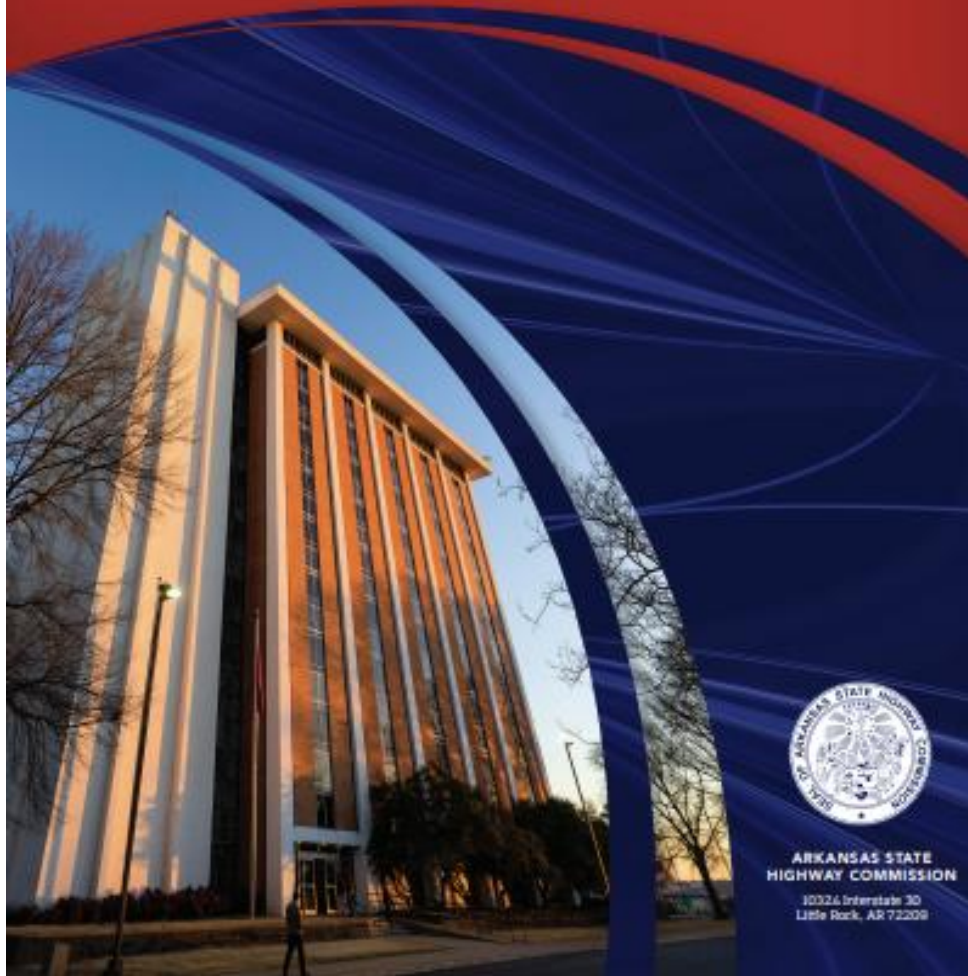

ARKANSAS STATE
HIGHWAY COMMISSION

10324 Interstate 30
Little Rock, AR 72209

Arkansas Legislative Council

EFFICIENCY STUDY RECOMMENDATIONS



Arkansas Department of Transportation
Arkansas Legislative Council
Efficiency Study Recommendations
Rules for Implementation

Arkansas Legislative Council

EFFICIENCY STUDY RECOMMENDATIONS

RECOMMENDATION #3

Publish status of construction projects and maintenance activities

- Solicited input from key ARDOT staff members and stakeholders regarding how information should be presented
- Garver is finalizing data connections and ARDOT-provided information into a draft dashboard for final approval



ARKANSAS STATE
HIGHWAY COMMISSION
10326 Interstate 30
Little Rock, AR 72209


Arkansas Legislative Council

EFFICIENCY STUDY RECOMMENDATIONS

RECOMMENDATION #10

Implement mid-term IT initiatives to optimize business operations

- Recommendation is now complete
 - ✓ Inventoried all applications and databases
 - ✓ Developed scoring system
 - ✓ Identified target state for each one
 - ✓ Used a phased approach for migration (either retain as-is, eliminate, re-engineer or migrate to a more modern platform)

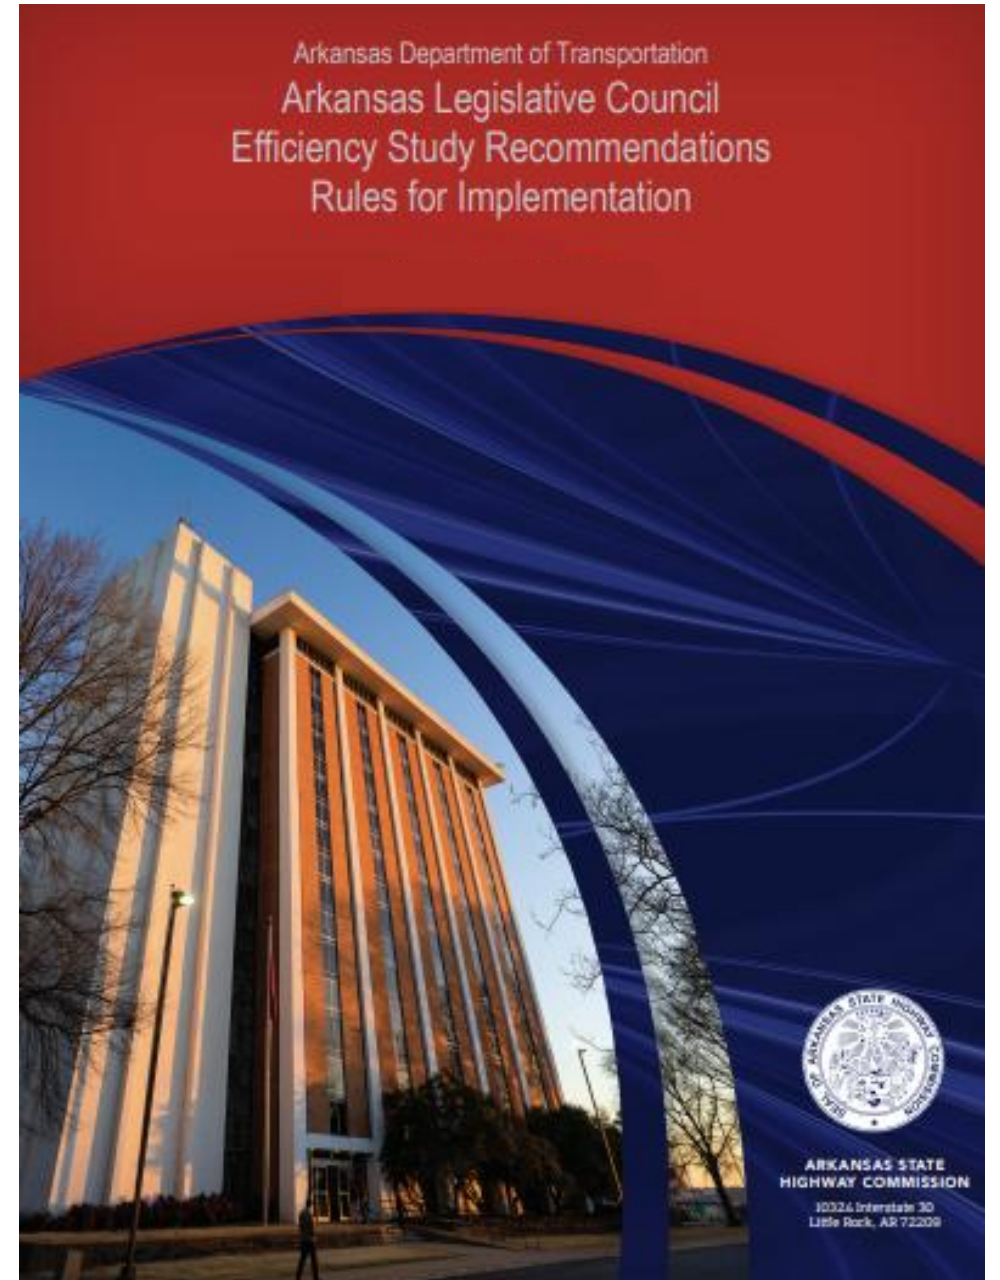

Recommendation		Number of Rules	Number of Rules Completed	Percent Complete
1	Finalize KPIs and implement performance management	7	6	86%
2	Strengthen knowledge management in anticipation of increased retirement	5	5	100%
3	Publish status of construction projects and maintenance activities	6	3	50%
4	Implement a platform that tracks all stakeholder inquiries to resolution	8	8	100%
5	Implement efficiencies in procurement and purchasing	10	7	70%
6	Implement construction contractor performance measurement	9	3	33%
7	Implement project and portfolio management frameworks	12	7	58%
8	Implement best practices in construction project design	3	2	67%
9	Build an IT Governance Structure to guide the Department's IT investments	7	6	86%
10	Implement mid-term IT initiatives that can optimize business operations	6	6	100%
11	Develop critical pillars necessary to establish IT as an effective business partner	5	5	100%
12	Ensure staff can develop in their careers at the Department	12	12	100%
13	Improve staff capabilities to align with current/future organizational needs			
Total		90	70	78%


Bid Letting Update

Keli Wylie, P.E.


Assistant Chief Engineer – Program Delivery



Interstate 49 CRAWFORD & SEBASTIAN COUNTIES

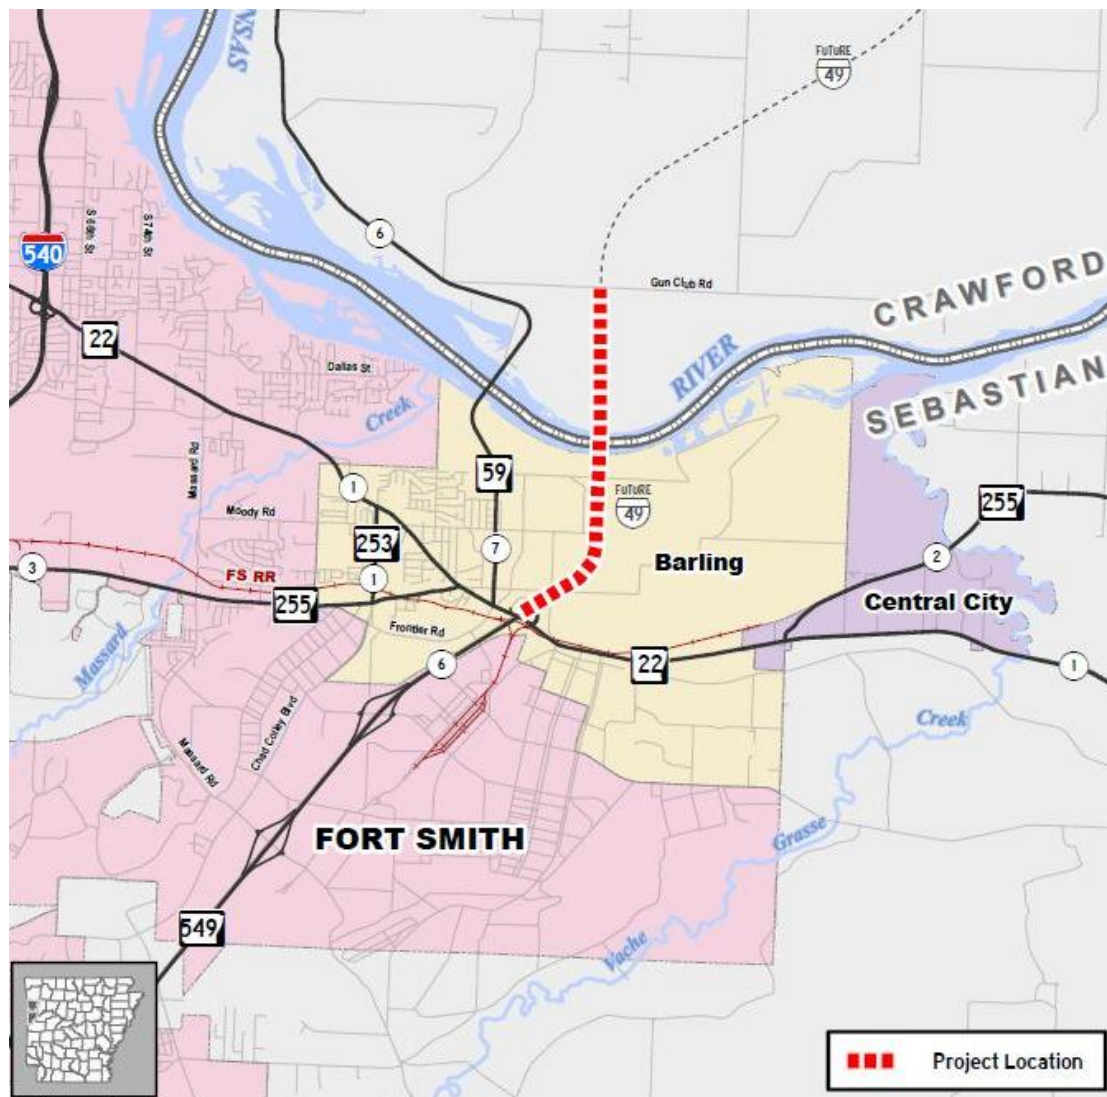

- New Location
- 3.2 Miles
- \$282.5 Million
- Manhattan Road & Bridge Co.
- Estimated Completion: Late 2029

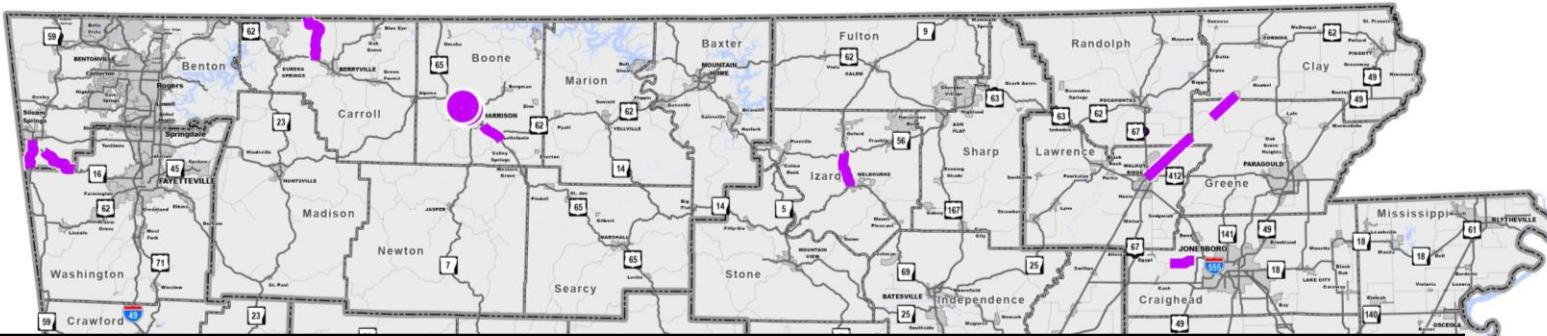

Bid Letting Update

NOVEMBER 6, 2024 LETTING RESULTS

Type of Projects	Number of Projects	Award Amount
State	24	\$ 93.7 Million
County	-	-
City	-	-
Total	24	\$ 93.7 Million

Awarded Projects

NOVEMBER 6, 2024 BID LETTING



● State Jobs


Project Not Shown

Job 012506
Districts 1, 5 & 10 Raised Pavement Markers (2025) (S)

Job 012508
Districts 4 & 9 Raised Pavement Markers (2025) (S)



Highway 64 SEBASTIAN COUNTY

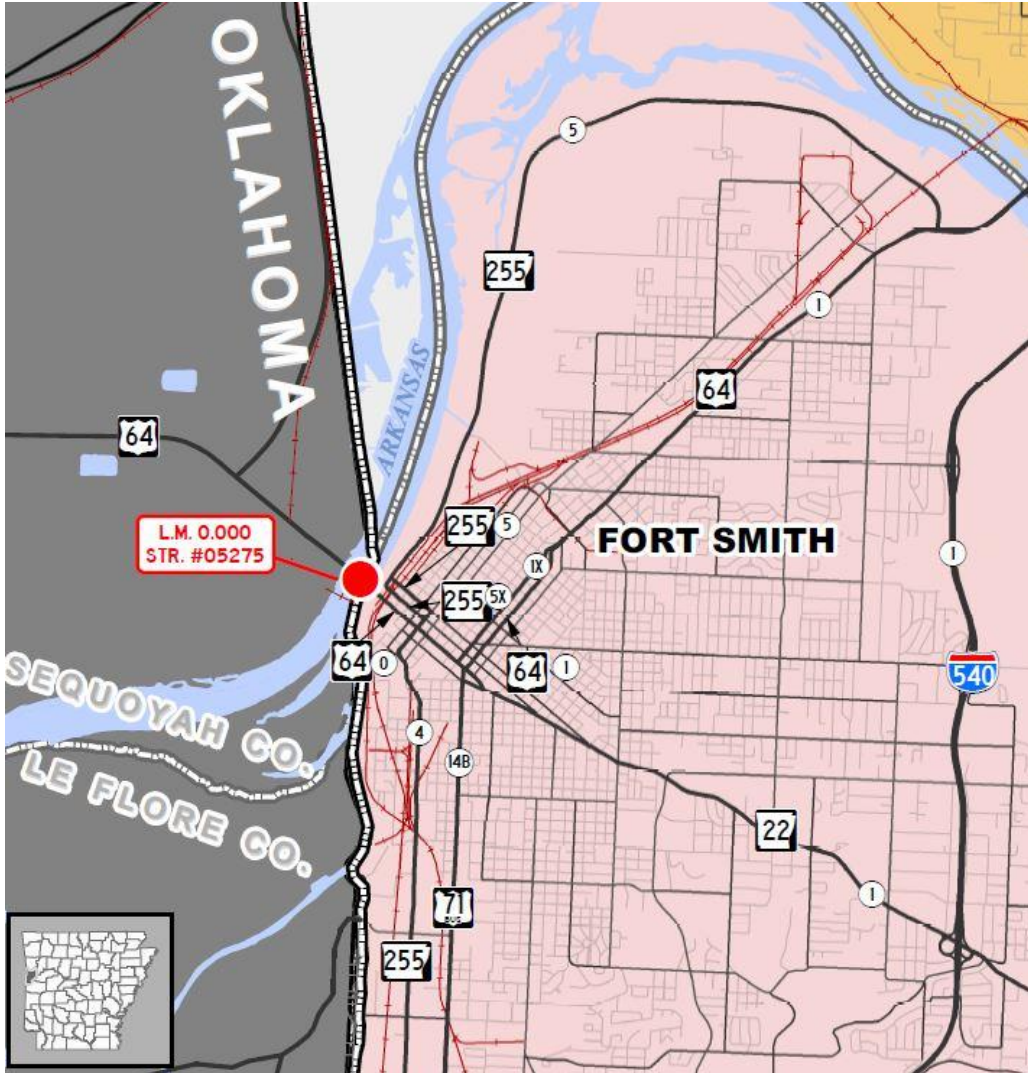


- Bridge Preservation
- \$3.7 Million
- Elite Industrial Painting, Inc.
- Estimated Completion: Late 2026




Highway 65 BOONE COUNTY

- Intersection Improvements & Signal Coordination
- 3 Intersections
- \$2.3 Million
- Crouse Construction, Co.
- Estimated Completion: Early 2026

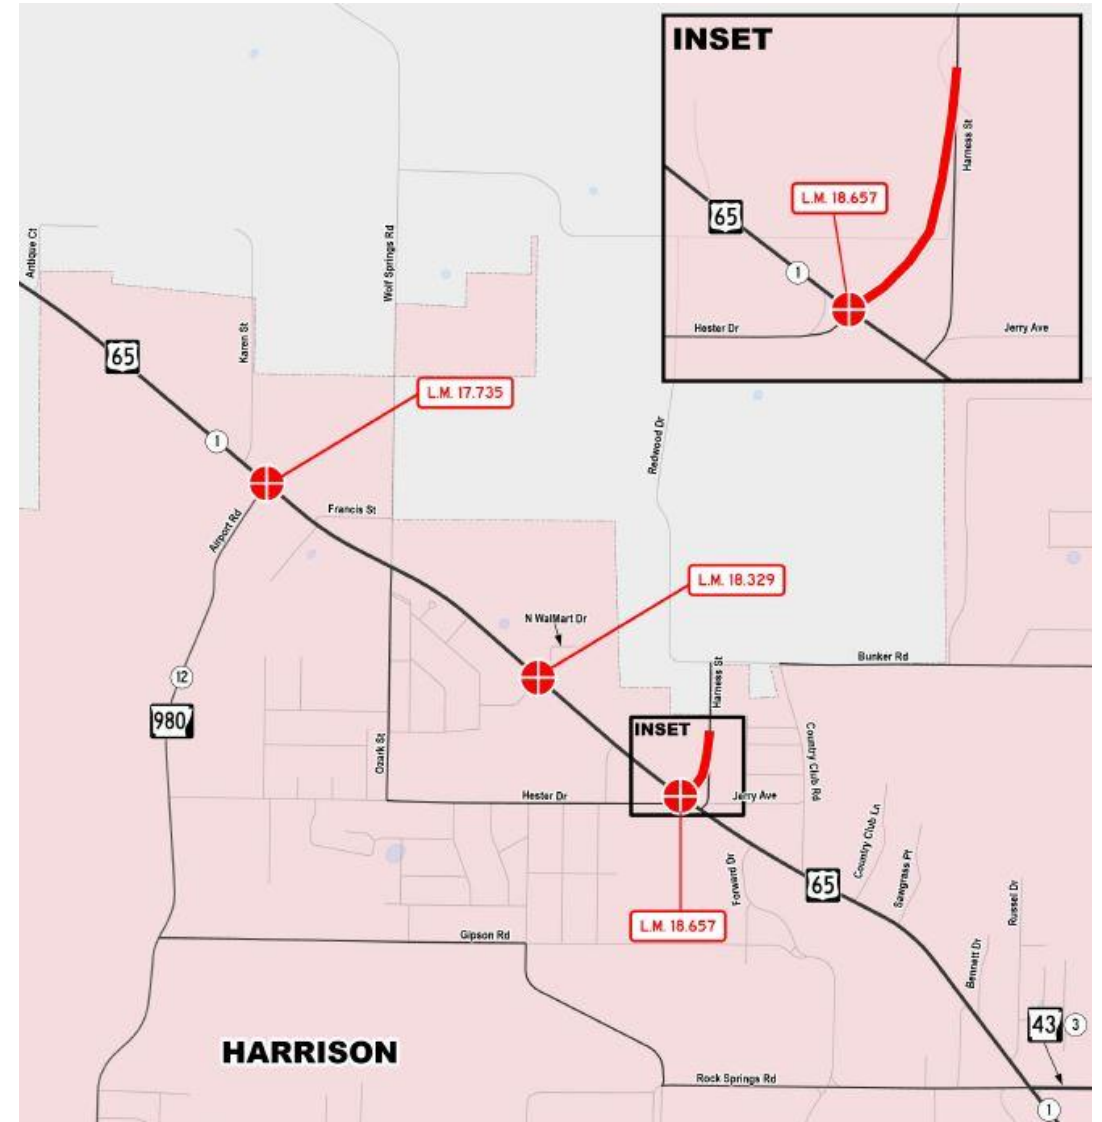



Highway 118 POINSETT COUNTY

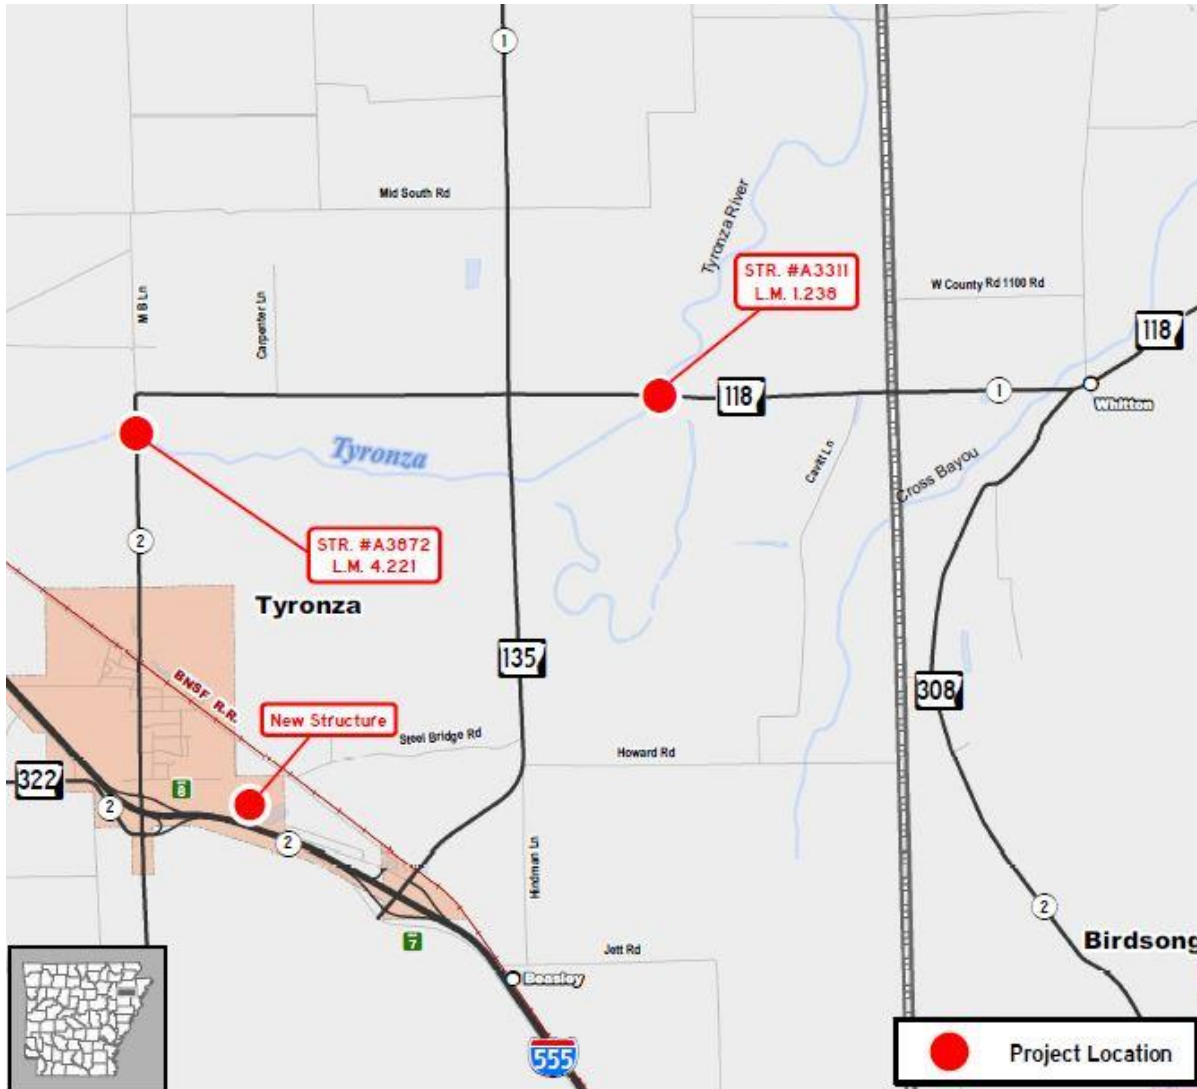

- 2 Bridge Replacements
- 1 New Bridge
- \$15.2 Million
- Robertson Contractors, Inc.
- Estimated Completion: Late 2027

Maintenance Activities

Rex Vines, P.E.


Chief Engineer – Operations

ARDOT

Maintenance Activities



Sweeping
Pipe Culverts
Patching
Ditch Cleaning
Milling
Drop Inlets
Signs
Guardrail
Litter & Debris
Snow & Ice
Levelling
Mowing
Joint Repair
Cable Barrier

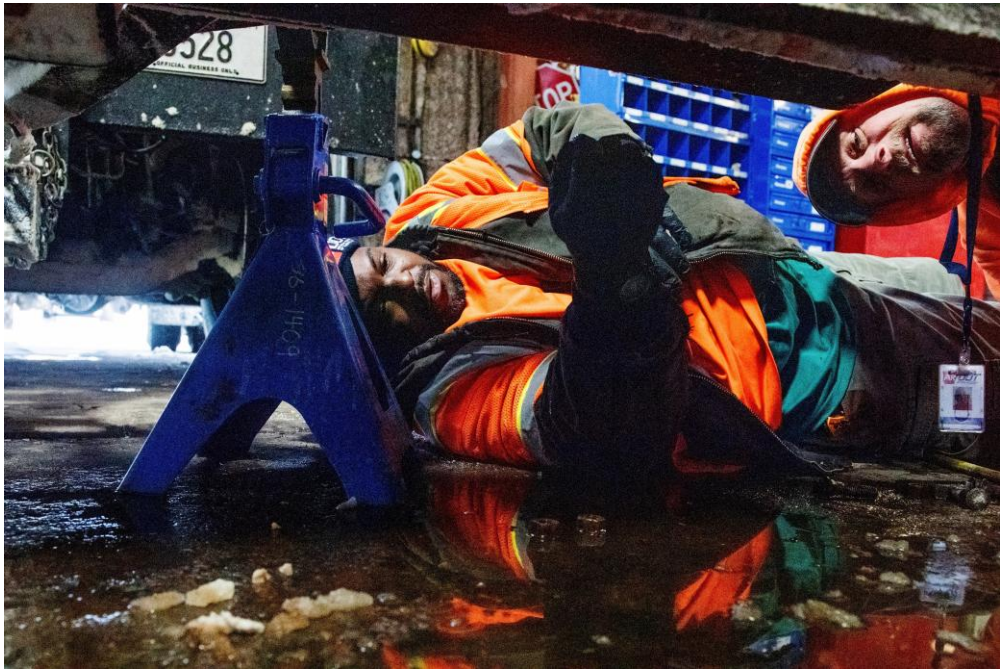

Maintenance Activities

WINTER WEATHER | TRAINING



Maintenance Activities


WINTER WEATHER SALT STORAGE

121 Salt Storage
Locations

84,000 Tons of Salt



Salt Storage Locations

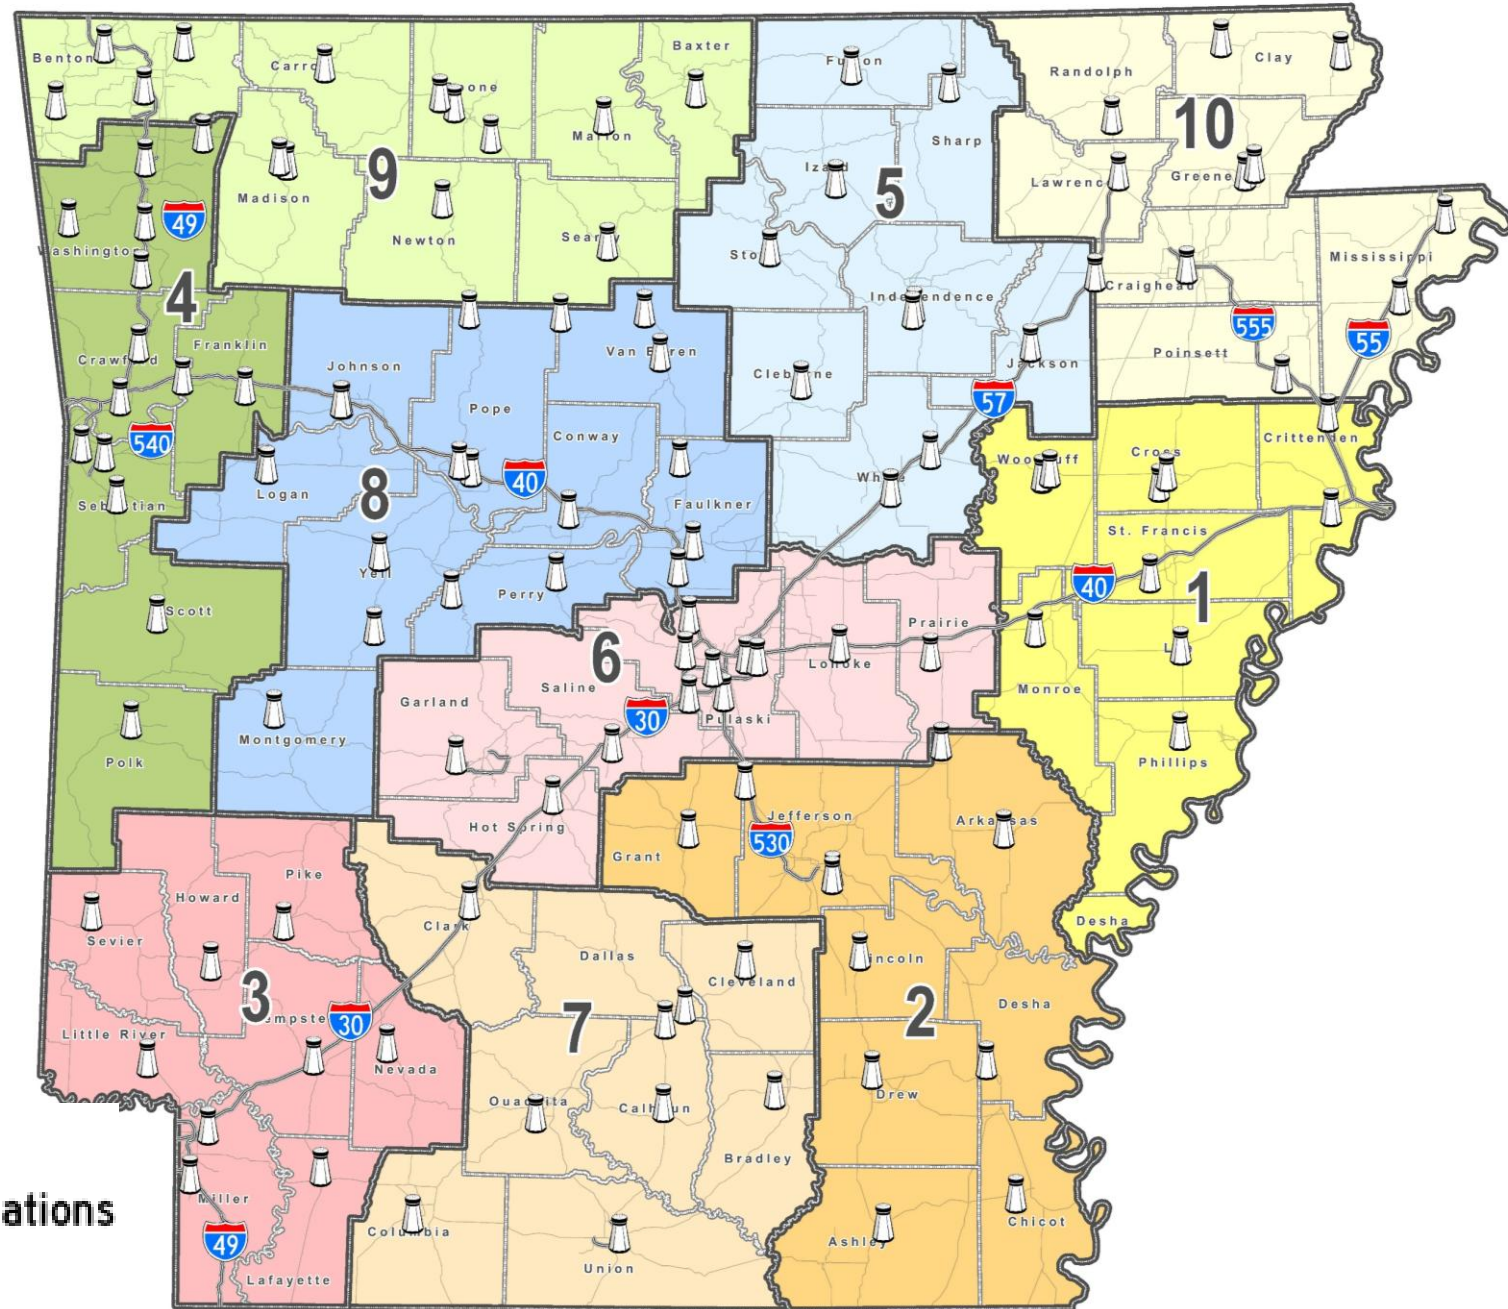

Maintenance Activities

ASPHALT PAVING | STATE CAPITOL



Recent Department Activities

Joint Committee on Transportation

OCTOBER 3, 2024




Conway Business Expo

OCTOBER 10, 2024



Interstate 57 Designation

NOVEMBER 7, 2024

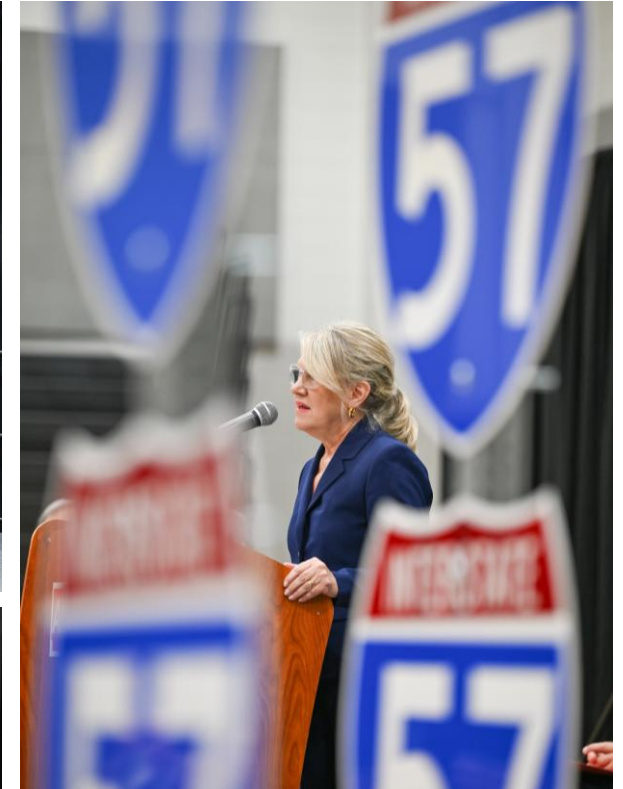



INTERSTATE

57

Corning Bypass Groundbreaking

NOVEMBER 14, 2024



Springdale Rotary Club

NOVEMBER 18, 2024



Good Roads Annual Meeting

NOVEMBER 20, 2024



30 Crossing Ribbon Cutting

DECEMBER 3, 2024





04

Consultant Selections

A. On-Call Bat Surveys

Consultant Selection

ON-CALL BAT SURVEYS | 2025-2029

Eight (8) Letters of Interest Received

All Firms Evaluated by ARDOT's Evaluation Committee

Recommendation to Begin Negotiations with Six (6) Firms

Civil & Environmental Consultants, Inc.
Franklin, TN

Copperhead Environmental Consulting, Inc.
Paint Lick, KY

Environmental Consultants of Habitats and Organisms, LLC
Tahlequah, OK

Environmental Solutions & Innovations, Inc.
Cincinnati, OH

Mitigation Surveying Services, Inc.
Benton, AR

Stantec Consulting Services, Inc.
Greenwood, AR

B. On-Call Cultural Resources

Consultant Selection

ON-CALL CULTURAL RESOURCES | 2025-2027

Fourteen (14)
Letters of Interest
Received

All Firms
Evaluated by
ARDOT's
Evaluation
Committee

Recommendation
to Begin
Negotiations with
Seven (7) Firms

Burns & McDonnell Engineering Company, Inc.
Springdale, AR

Chronicle Heritage
Memphis, TN

Cultural Resource Analysts, Inc.
West Fork, AR

Flat Earth Archeology, LLC
Cabot, AR

Johnson, Mirmiran & Thompson, Inc.
Brentwood, TN

Stantec Consulting Services, Inc.
Tulsa, OK

WSP USA, Inc.
Kansas City, MO

C. Independent Cost Estimating

Consultant Selection

ON-CALL INDEPENDENT COST ESTIMATING | 2025-2027

Five (5) Letters of Interest Received

All Firms Evaluated by ARDOT's Evaluation Committee

Recommendation to Begin Negotiations with Four (4) Firms

Elle Consultants, Inc.
Rancho Cordova, CA

Innovative Contracting & Engineering, PLLC
Highland, UT

Krebs Corporation
Park City, UT

Stanton Constructability Services, LLC
Holladay, UT

D. On-Call Design

Consultant Selection

ON-CALL DESIGN SERVICES

2025-2028

Forty (40) Letters
of Interest
Received

All Firms
Evaluated by
ARDOT's
Evaluation
Committee

Recommendation
to Begin
Negotiations with
Fifteen (15) Firms

AECOM Technical Services, Inc.
Little Rock, AR

Burns & McDonnell Engineering Co., Inc.
Springdale, AR

Crafton, Tull & Associates, Inc.
Rogers, AR

Garver, LLC
North Little Rock, AR

HDR Engineering, Inc.
Little Rock, AR

HNTB Corporation
Little Rock, AR

McClelland Consulting Engineers, Inc.
Fayetteville, AR

Michael Baker International, Inc.
Little Rock, AR

Modjeski and Masters, Inc.
New Orleans, LA

Neel-Schaffer, Inc.
Jackson, MS

NTB Associates, Inc.
Little Rock, AR

Pickering Firm, Inc.
Jonesboro, AR

TranSystems Corporation
Kansas City, MO

Universal Surveying & Mapping, LLC
Stillwater, OK

Volkert, Inc.
Little Rock, AR

05

Around the Department

Project Development – Part 2

Jared Wiley


Chief Engineer – Preconstruction



PROJECT DEVELOPMENT PROCESS


PART 2

PROJECT DEVELOPMENT MILESTONES

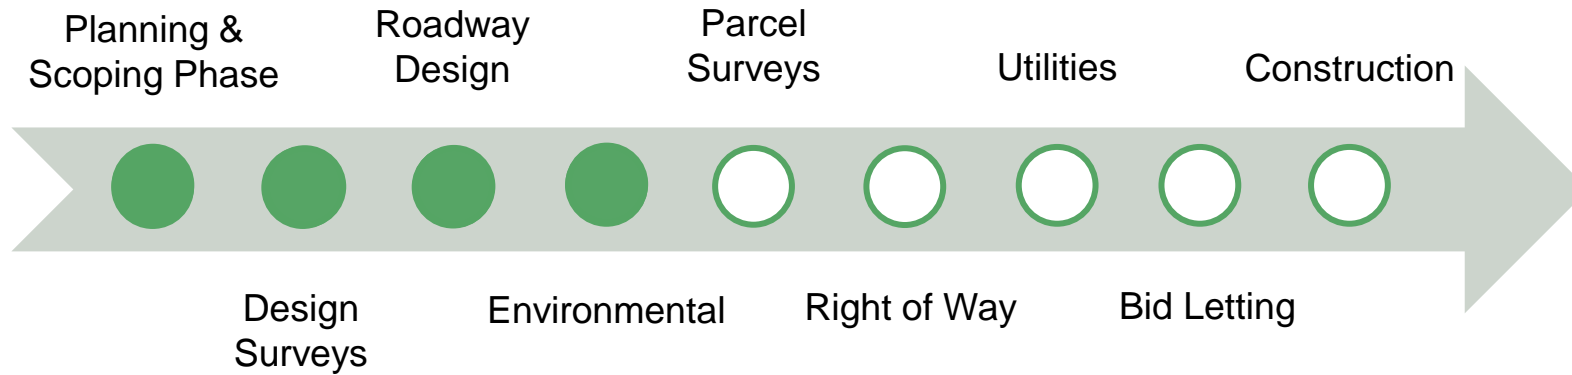


PROJECT DEVELOPMENT PROCESS


	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	60%	100%				
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27				
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

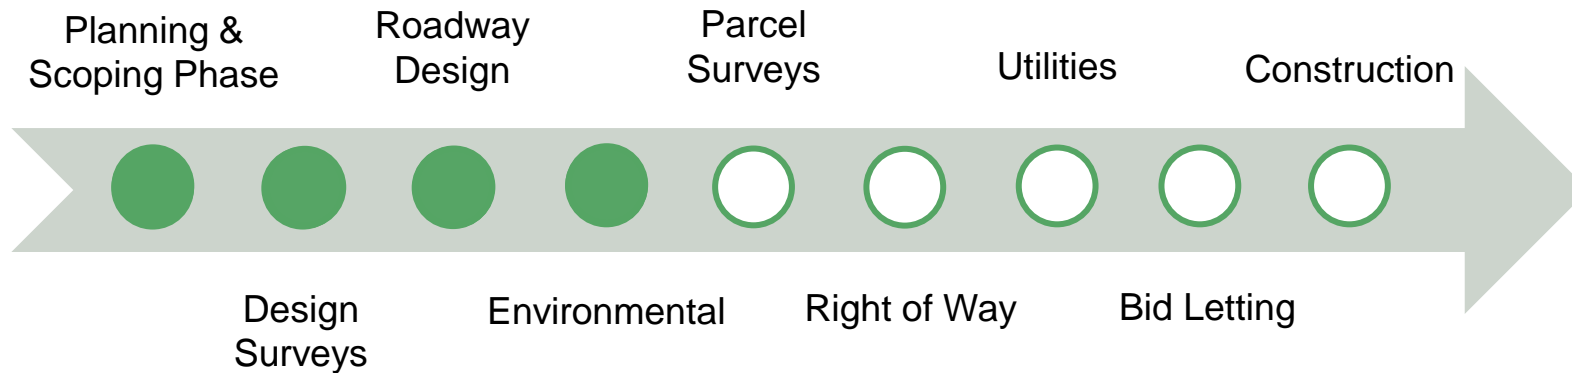

PARCEL SURVEYS

	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	60%	100%				
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27				
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

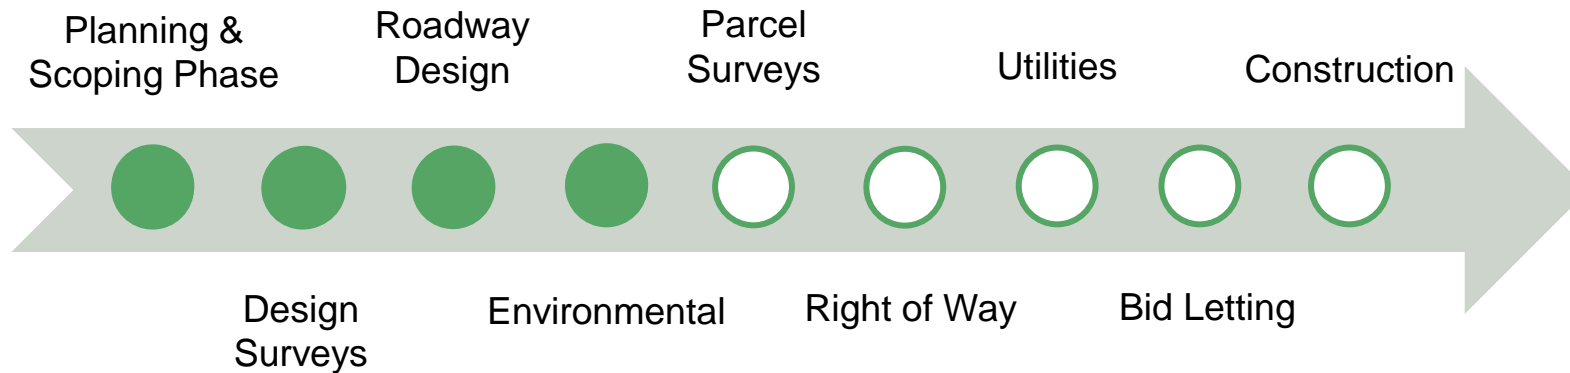

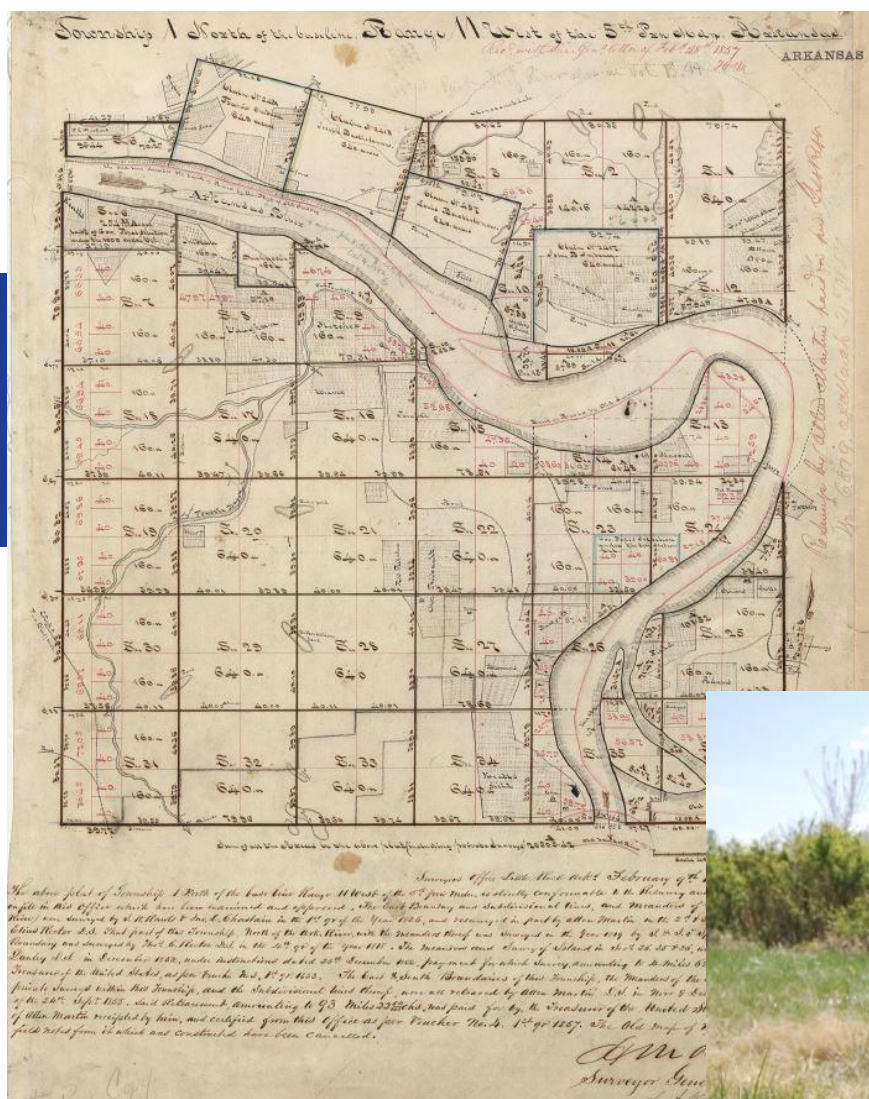


PARCEL SURVEYS

- Initiate title research, complete field reconnaissance, create parcel worksheets
- Complete 750 to 1,000 parcel surveys a year




PARCEL SURVEYS

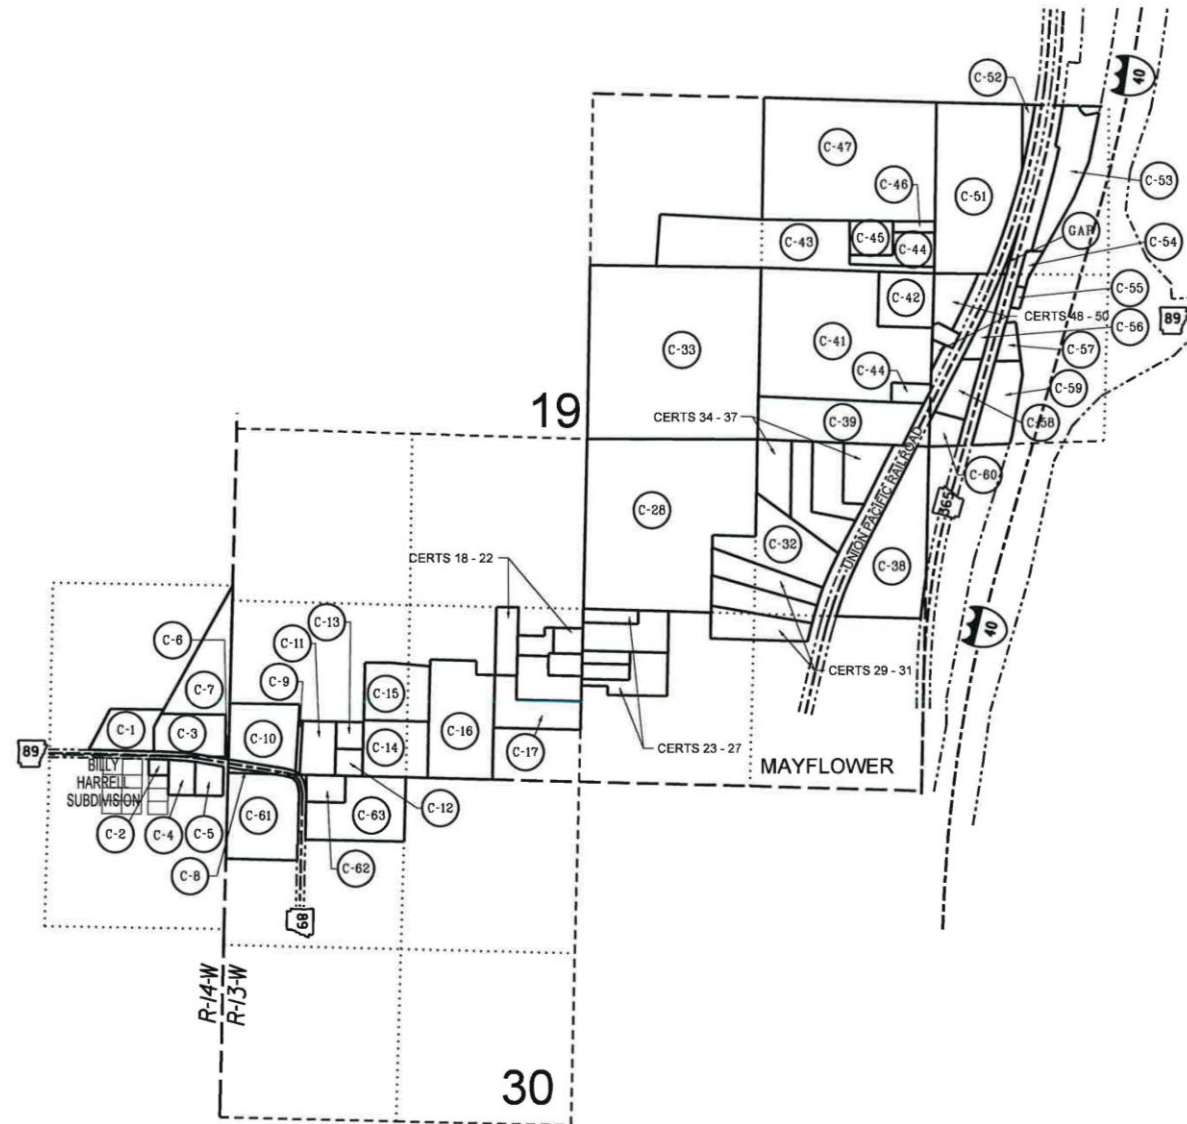


RIGHT OF WAY

	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	60%	100%	100%			
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26			
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

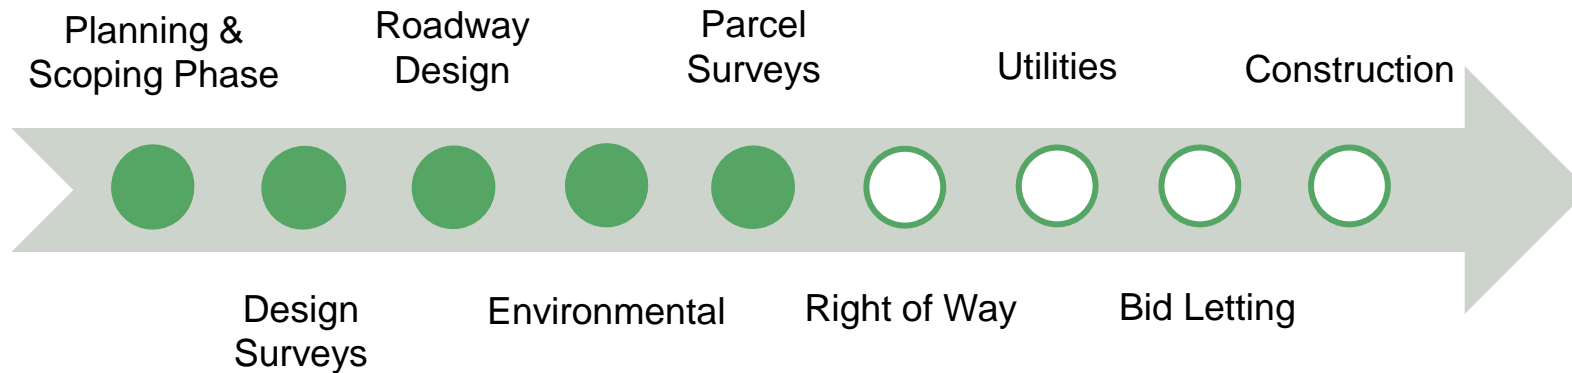

RIGHT OF WAY ENGINEERING & APPRAISALS

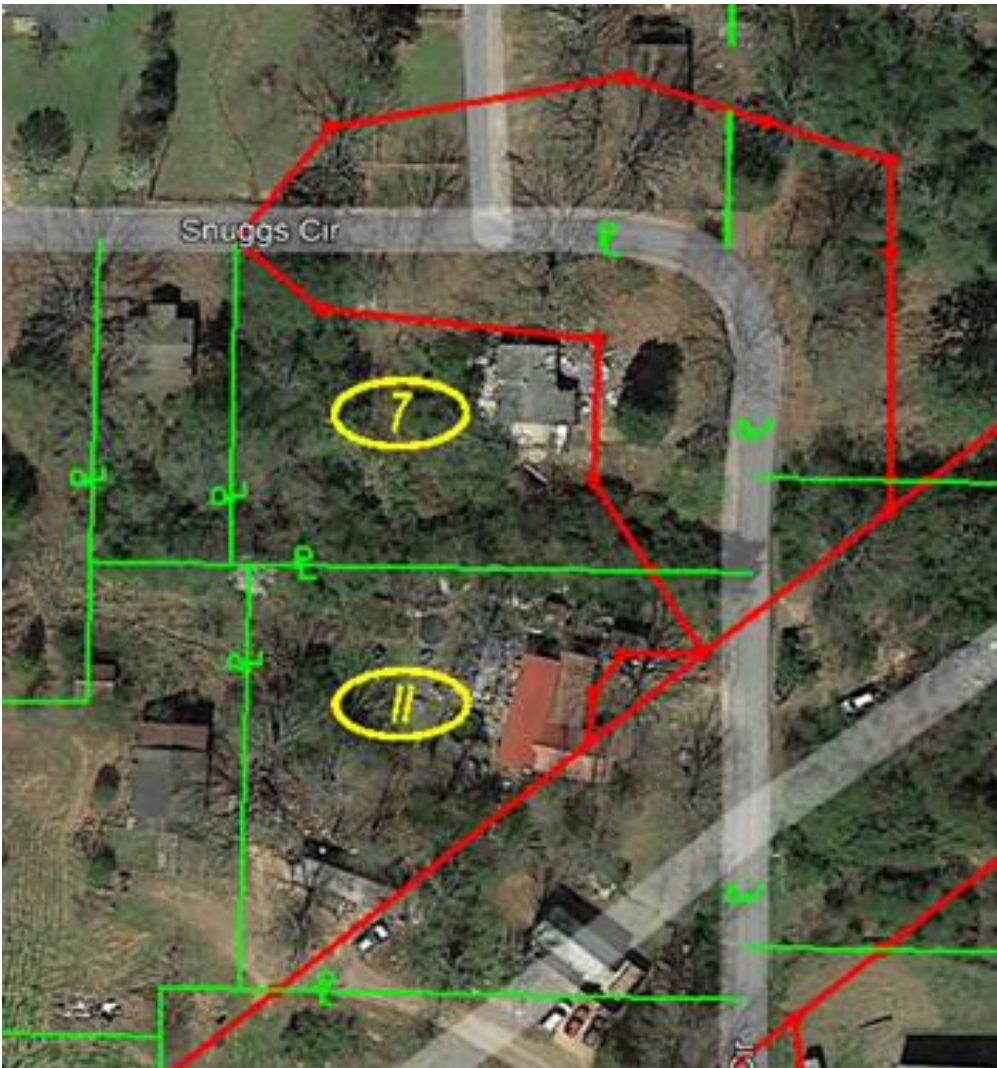

000000 TR1 Jon Doe

I-30
Little Rock, AR 72209


PREPARED BY:



AR DOT
ARKANSAS DEPARTMENT
OF TRANSPORTATION

Effective Date of Valuation November 27, 2024	Prepared For Arkansas Department of Transportation	Client File Number 000000
Date of the Report November 27, 2024	Example Pulaski	Internal File Number Tract 1
Report Type Appraisal Report		

RIGHT OF WAY ACQUISITION & RELOCATION

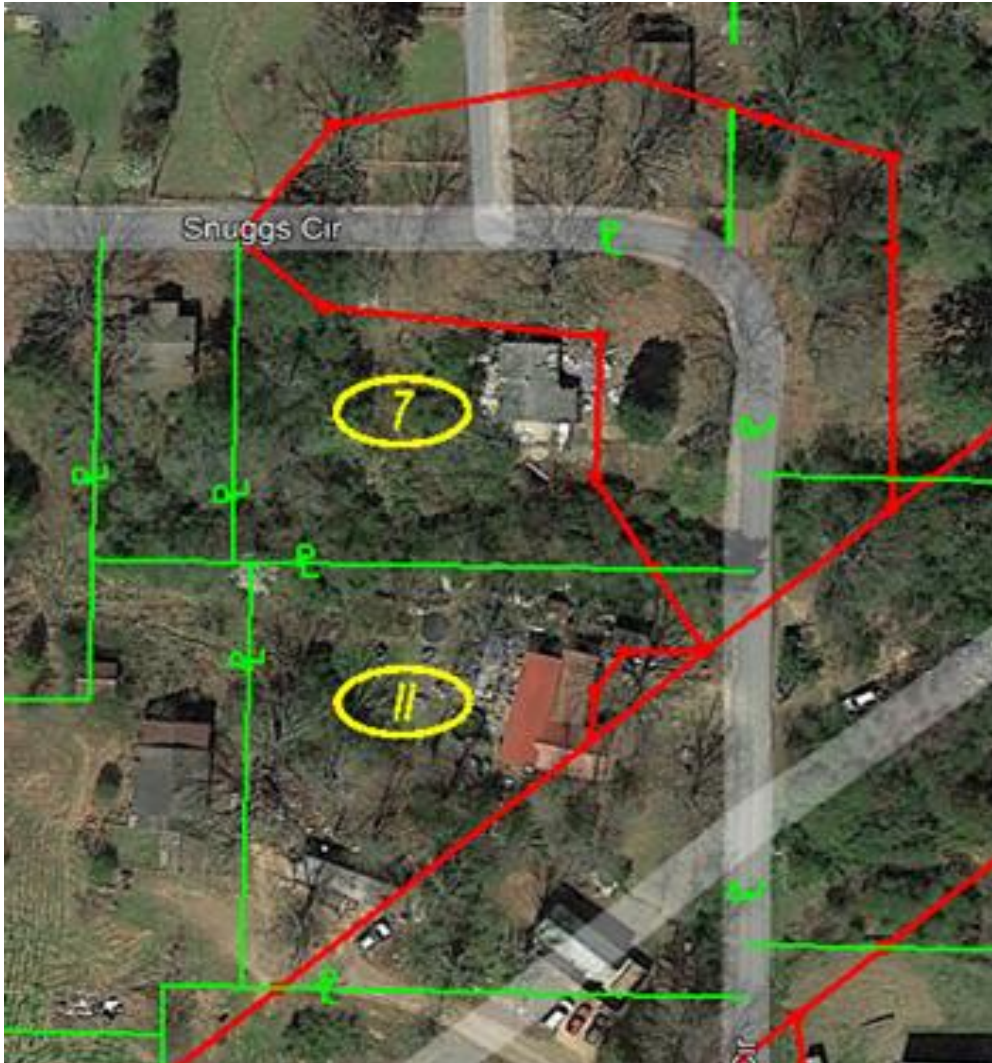


- 1,120 property tracts acquired in 2023
- Relocation assistance provided for displaced property owners

RIGHT OF WAY



UTILITIES

	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	60%	100%	100%	100%		
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28		
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

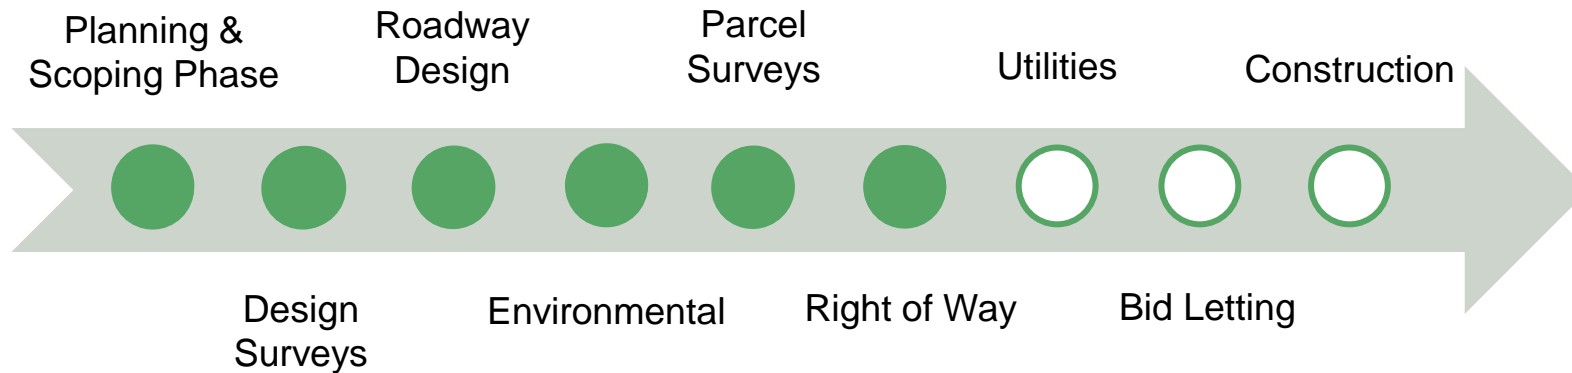



UTILITIES


- Coordinate with hundreds of utility owners annually
- Issued 1,457 regular utility permits in 2023
- Currently working on 458 projects in various stages



UTILITIES

REVISED SCHEDULE

	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	100%	100%	100%	100%	30%	
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Jun 30	Aug 30
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

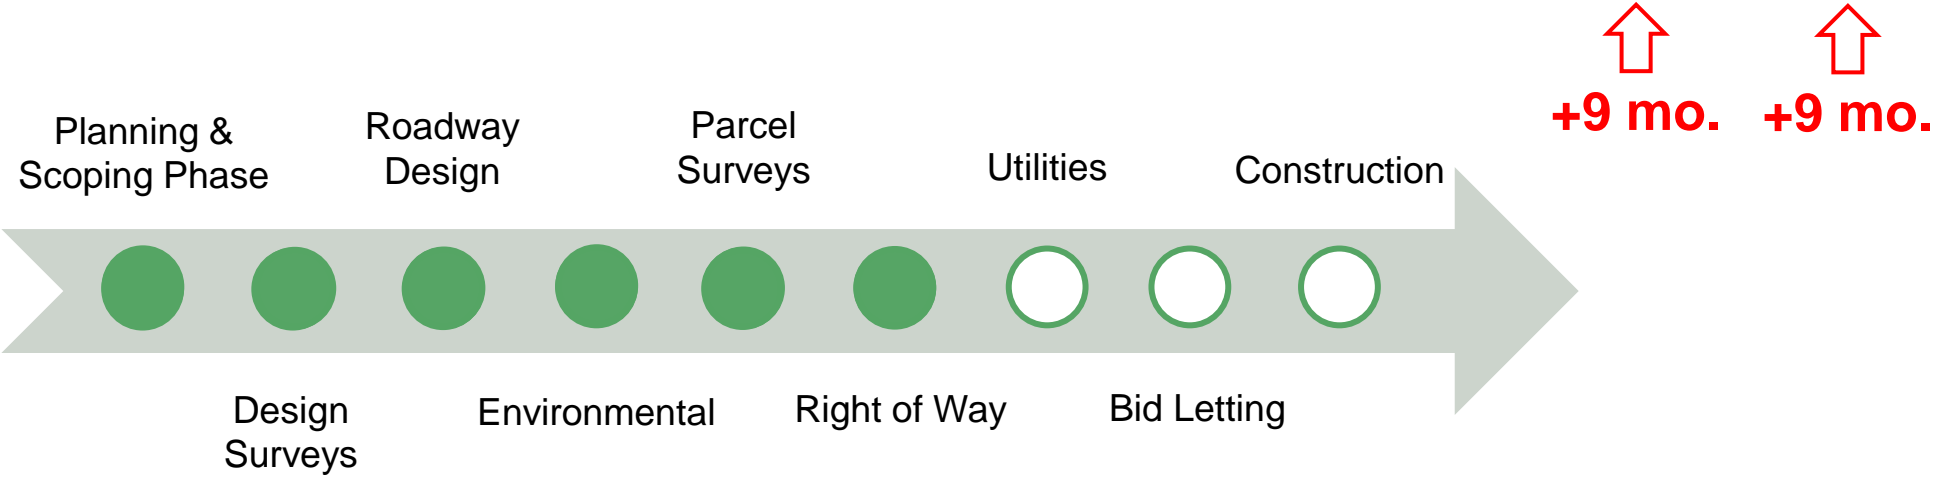



LETTING CALENDAR 2025

JANUARY						
S	M	T	W	T	F	S
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

FEBRUARY						
S	M	T	W	T	F	S
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	

MARCH						
S	M	T	W	T	F	S
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

APRIL						
S	M	T	W	T	F	S
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30			

MAY						
S	M	T	W	T	F	S
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

JUNE						
S	M	T	W	T	F	S
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

JULY						
S	M	T	W	T	F	S
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

AUGUST						
S	M	T	W	T	F	S
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

SEPTEMBER						
S	M	T	W	T	F	S
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

OCTOBER						
S	M	T	W	T	F	S
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

NOVEMBER						
S	M	T	W	T	F	S
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

DECEMBER						
S	M	T	W	T	F	S
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

Advertise
Commission Meeting - Little Rock
Bid Letting - Little Rock

Holiday
Go List
Status List
Staff Meeting
Printing Staff Minutes


BID LETTING

Pre-Advertisement To-Do List


- Final Plans & Specifications
- Engineer's Estimate
- Environmental Status
- Right of Way & Utilities Status
- Funding Prepared

BID LETTING

	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	100%	100%	100%	100%	130%	
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Jun 30	Aug 30
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

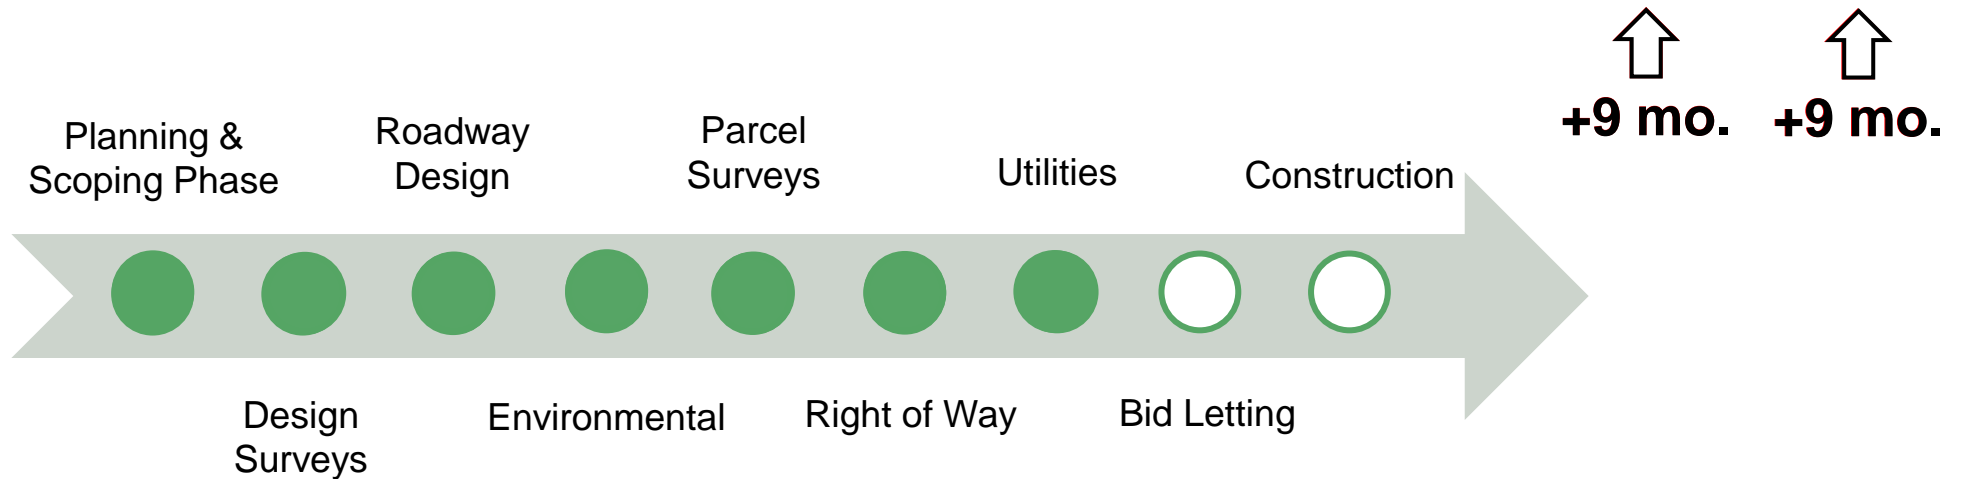


BID LETTING

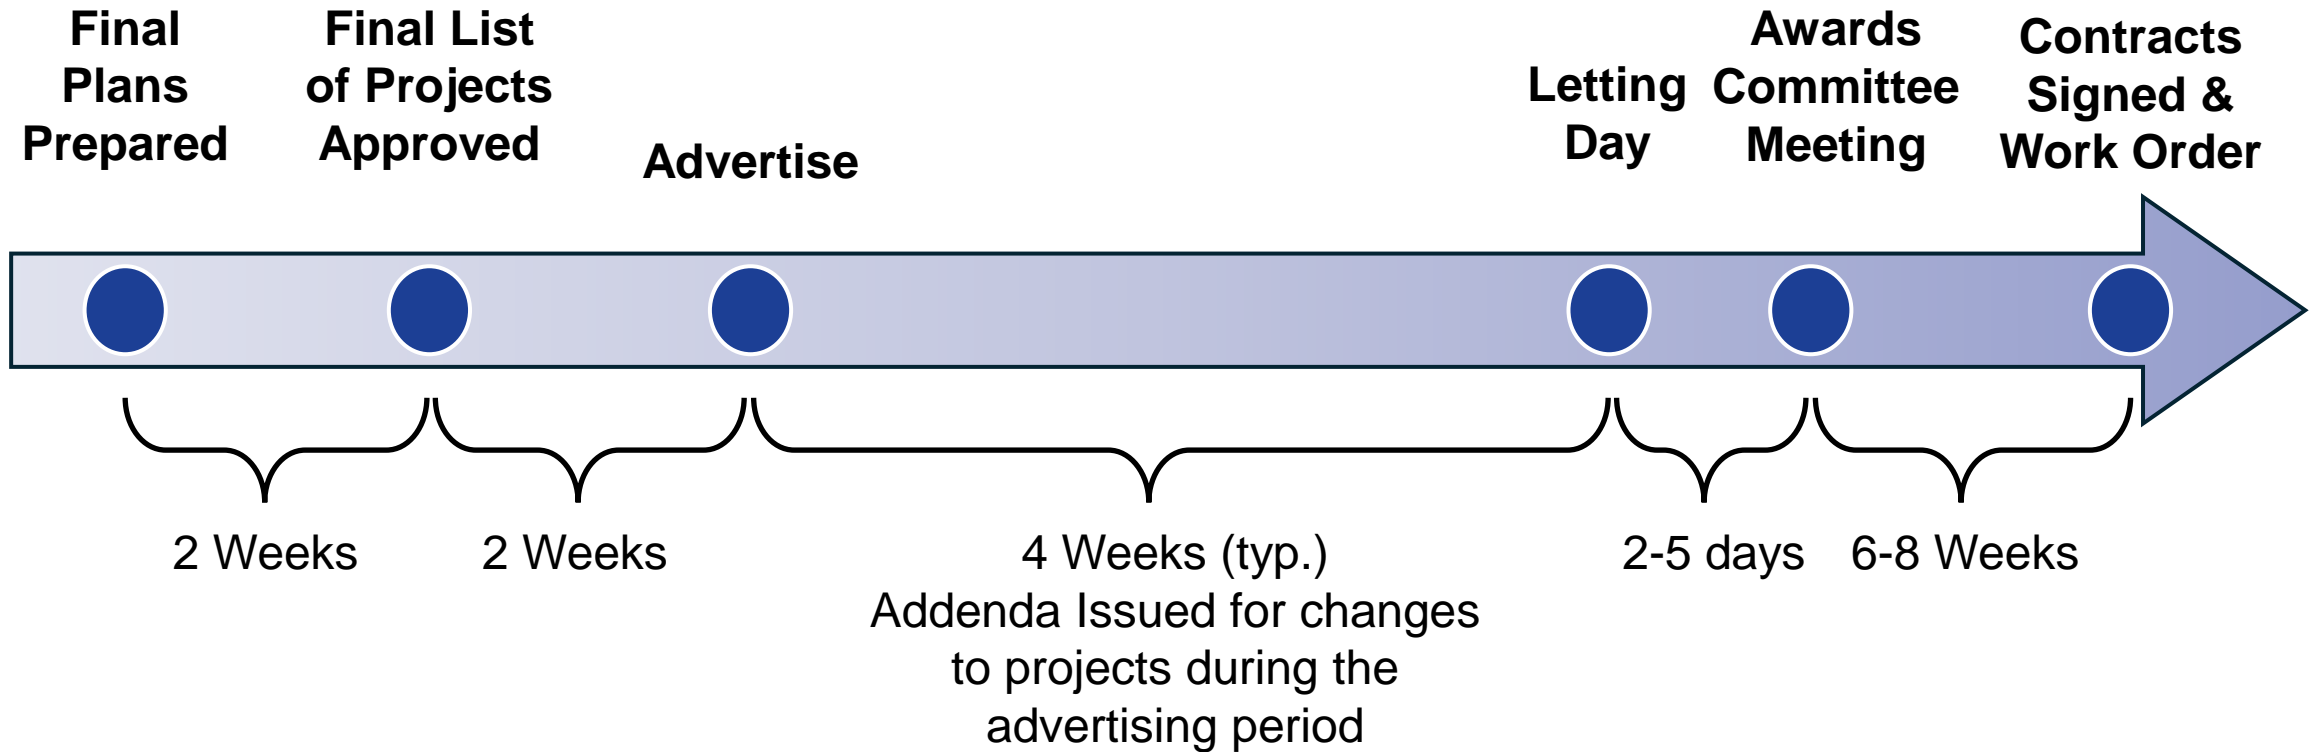

PROJECT AWARDED

	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	100%	100%	100%	100%	100%	100%
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Jun 30	Aug 30
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

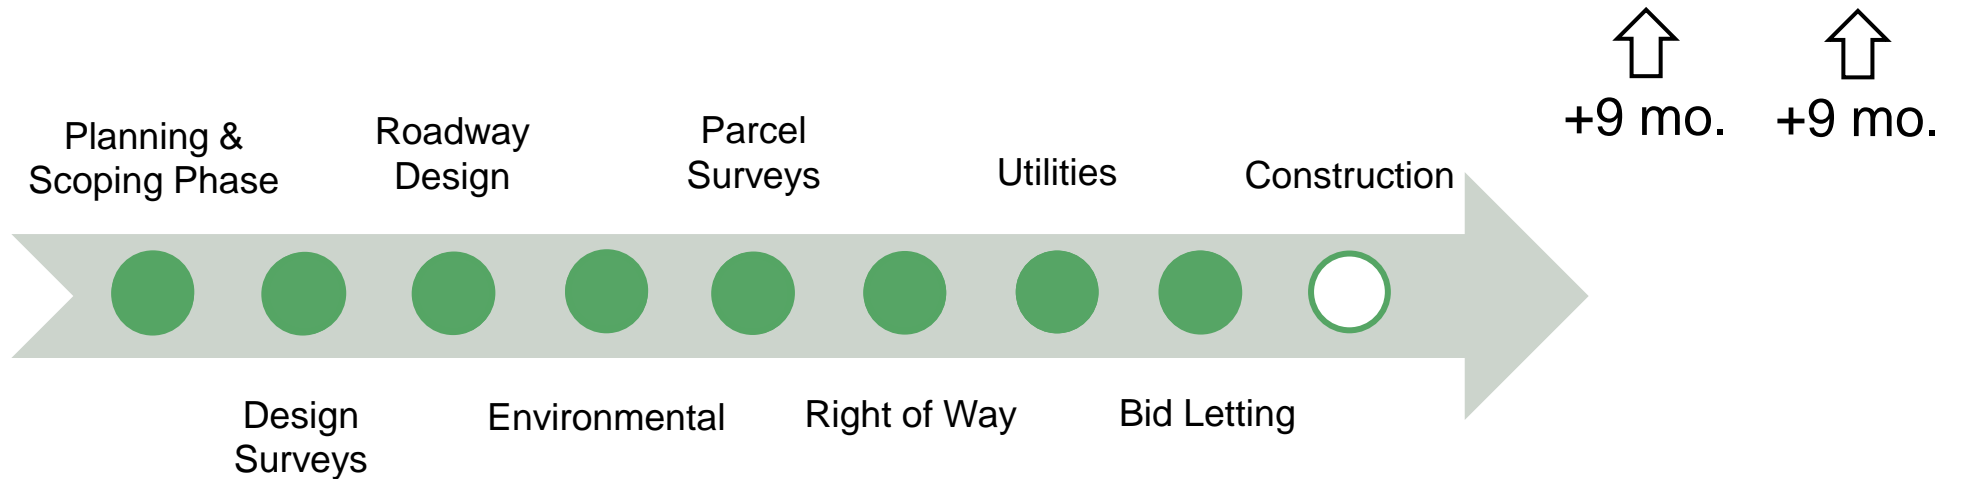

CONSTRUCTION


185 Active Projects


Total \$3.4 Billion



CONSTRUCTION

	PLAN	DSUR	RDWY	ENV	PSUR	ROW	UTIL	LET
PERCENT COMPLETE	100%	100%	100%	100%	100%	100%	100%	100%
TARGET DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Sep 29	Nov 29
END DATE	Jun 25	Mar 26	Dec 26	Jun 27	Jul 26	Sep 28	Jun 30	Aug 30
DURATION	6 mo.	9 mo.	9 mo.	6 mo.	4 mo.	12 mo.	12 mo.	

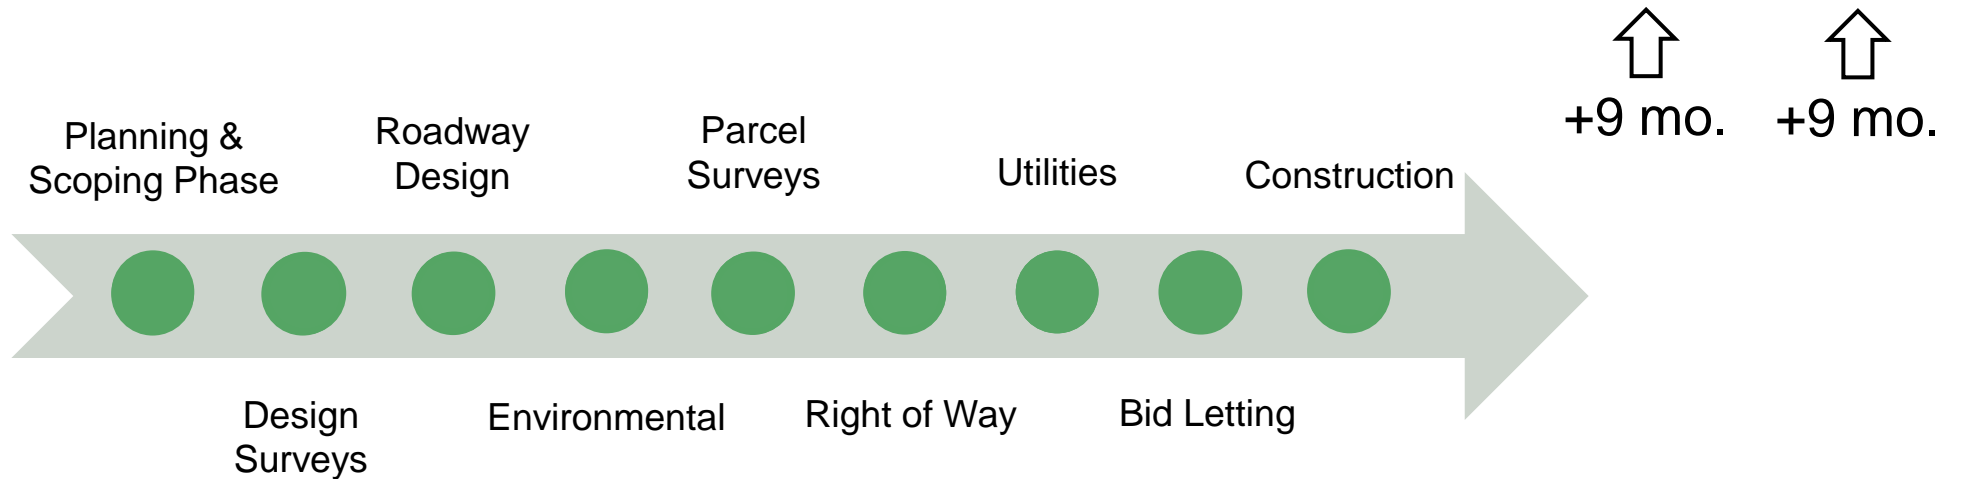

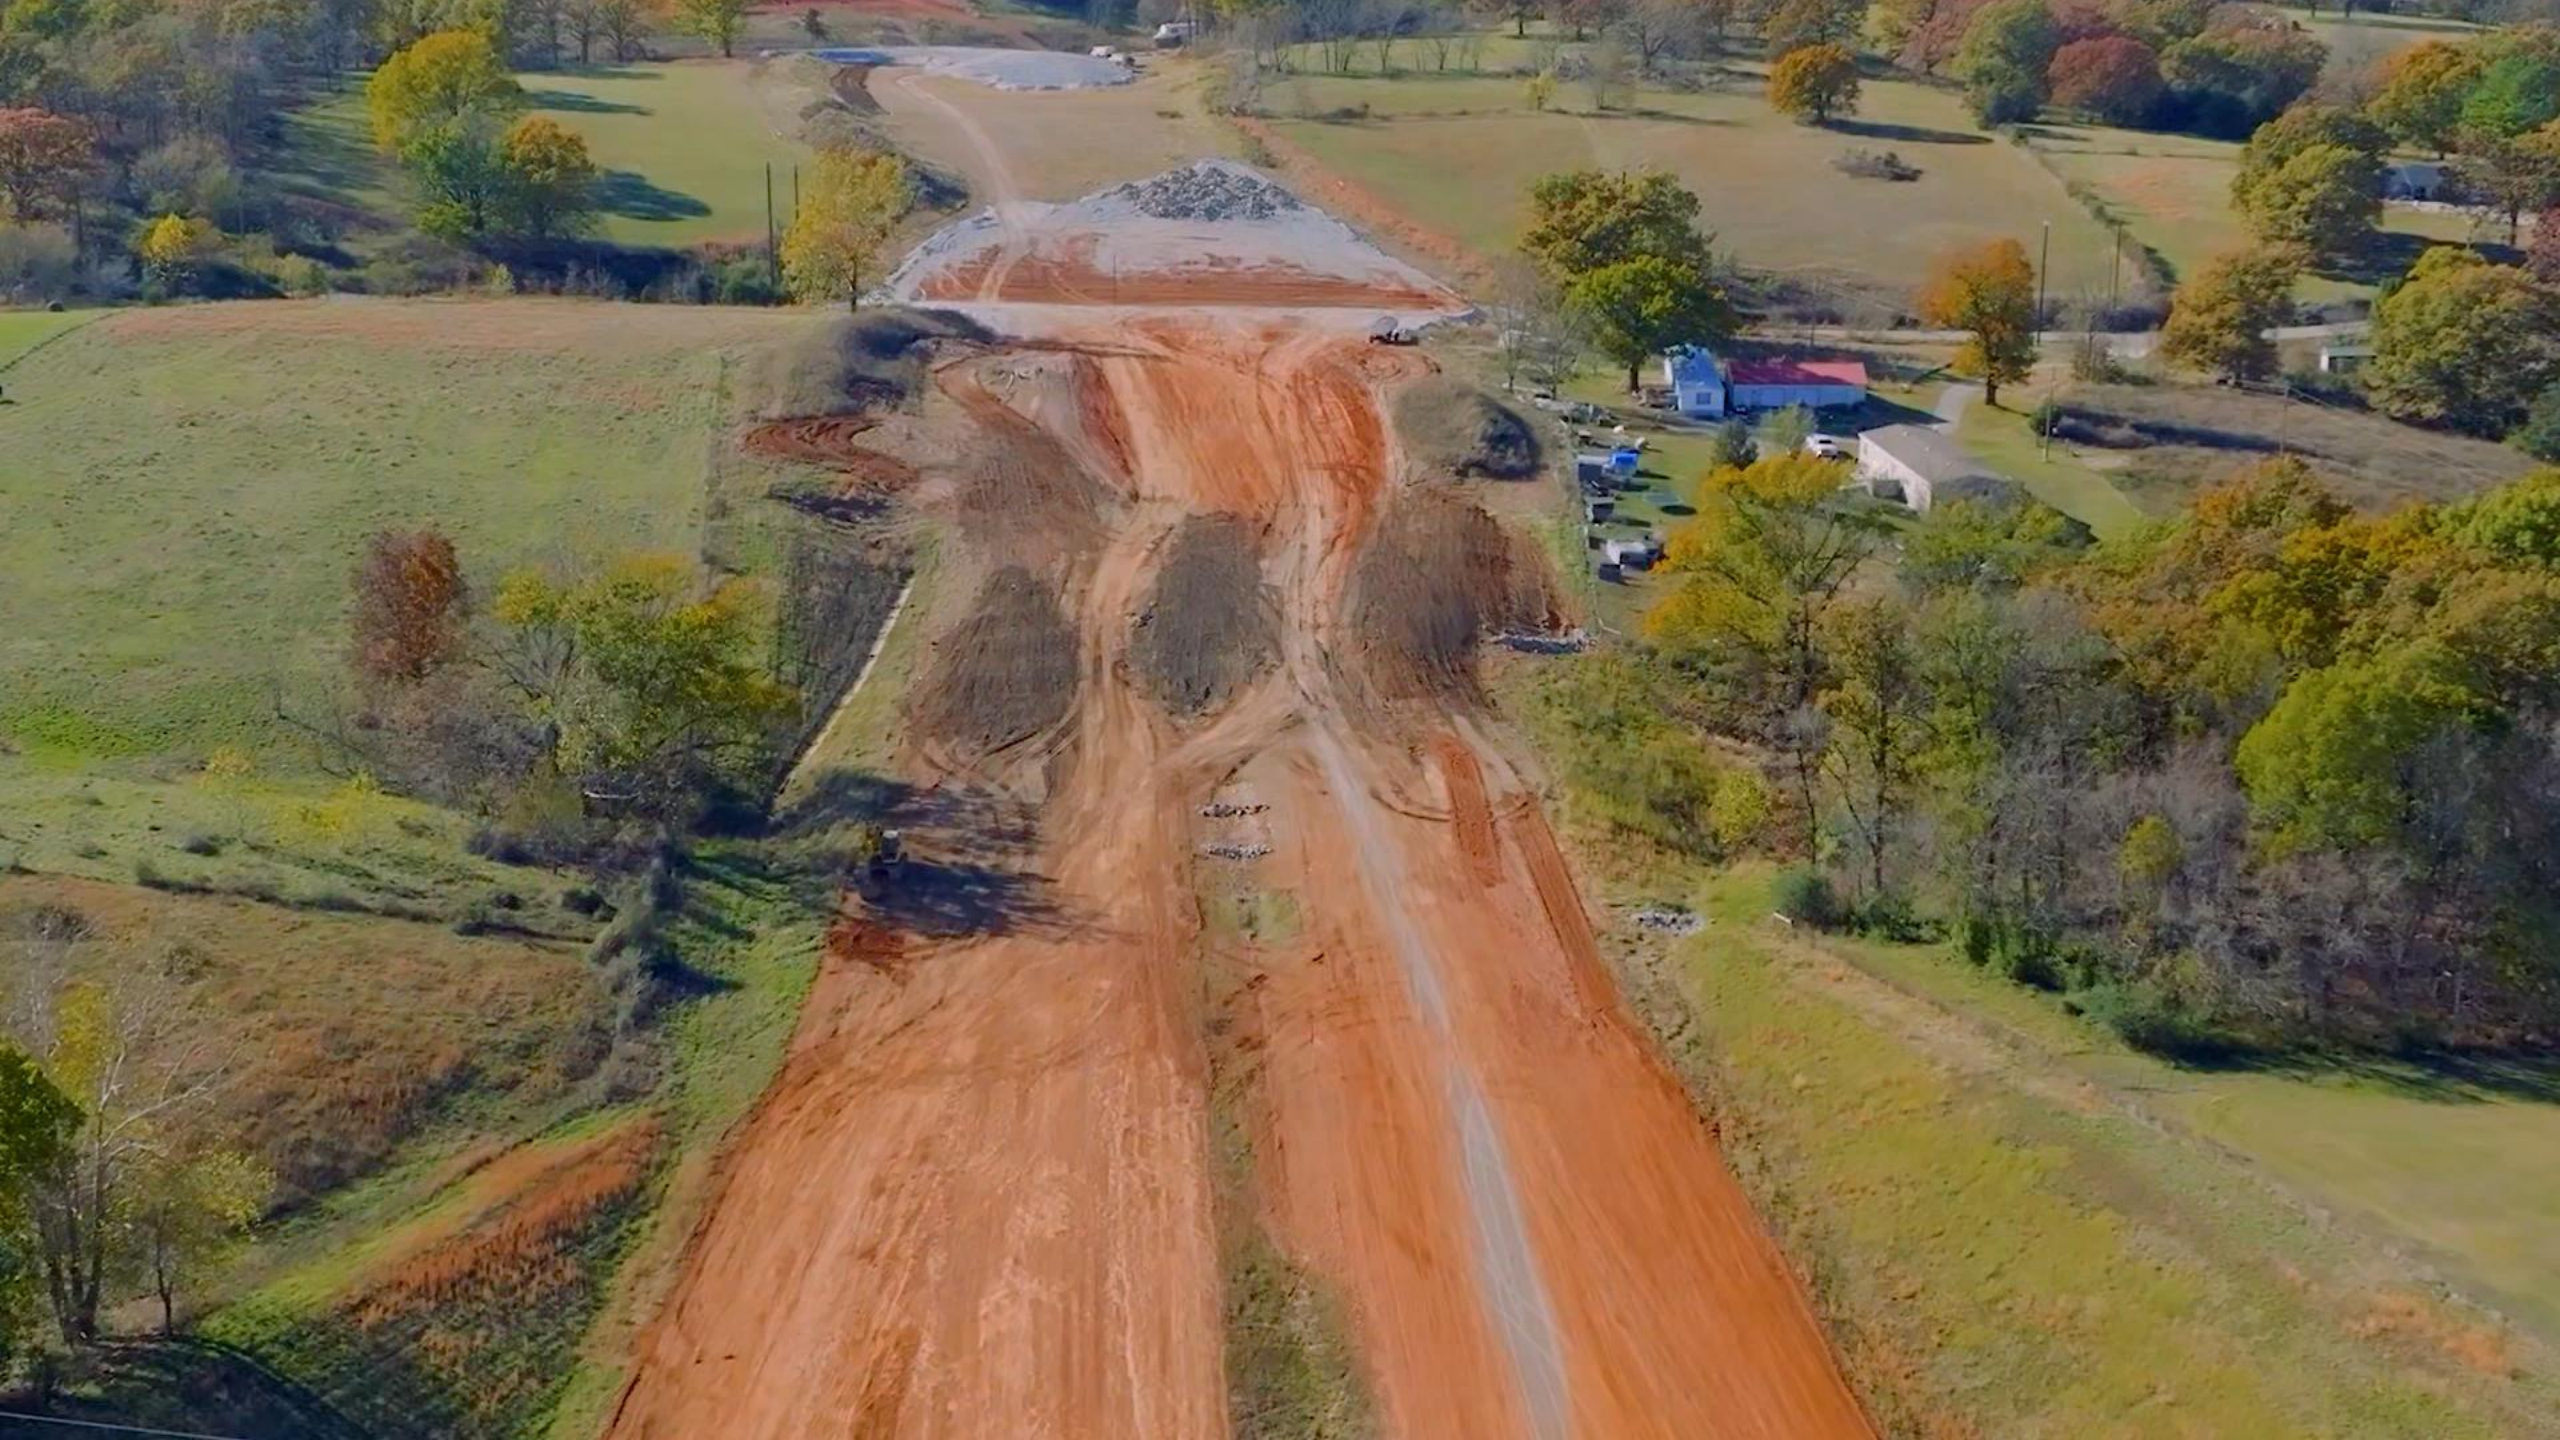



PROJECT DEVELOPMENT PROCESS

PART 2

06

Upcoming Events

UPCOMING Events

DECEMBER 11

Retirement Board Christmas Dinner

Director Tudor
5:00 PM | Little Rock

DECEMBER 17

Utility Relocation Reform

Director Tudor & Vice Chairman Taldo
2:00 PM | Central Offices

DECEMBER 18

**Highway Commission Review & Advisory
Subcommittee Meeting**

Director Tudor
3:00 PM | Little Rock, AR

DECEMBER 24

Christmas Eve Holiday

DECEMBER 25

Christmas Day Holiday

JANUARY 1

New Year's Day Holiday

UPCOMING Events

JANUARY 9

AAPA Technical Conference

Director Tudor
1:20 PM | Little Rock, AR

JANUARY 15

Legislator Orientation

Director & Staff
2:30 PM | Central Office

JANUARY 16

Meeting with Holly Springs

Director & Staff
6:00 PM | Holly Springs, AR

JANUARY 20

MLK Jr. Day Holiday

FEBRUARY 6

**Northwest Arkansas Board of Realtors
Meeting**

Vice Chairman Taldo
11:30 AM | Lowell, AR

FEBRUARY 10-13

Washington Briefing

TBD
Washington, DC

UPCOMING
Events

FEBRUARY 17

President's Day Holiday

FEBRUARY 19

Highway Commission Meeting

Director & Commissioners
10:00 AM | Central Offices

ARDOT DISTRICT SERVICE AWARDS

DECEMBER 5

District 5

Batesville Community Center
10:00 AM

DECEMBER 6

District 9

District 9 Headquarters
11:00 AM

DECEMBER 9

District 2

White Hall Community Center
11:00 AM

DECEMBER 10

District 1

Technology Center for the Delta - Wynne
10:30 AM

DECEMBER 11

District 8

Dardanelle Community Center
11:00 AM

DECEMBER 12

District 7

Calvary Baptist Church - Camden
10:00 AM

DECEMBER 13

District 10

Paragould Community Center
10:30 AM

DECEMBER 16

Maintenance Division

ARDOT Sign Shop
11:00 AM

DECEMBER 17

Central Office

ARDOT Central Office Auditorium
10:00 AM

DECEMBER 18

District 6

Geyer Springs Baptist Church
10:30 AM

DECEMBER 19

District 4

District 4 Headquarters
11:00 AM

DECEMBER 20

District 3


District 3 Headquarters
11:00 AM

07


**Other Business and
Discussion**

FY 2025 RAISE Grant Program RECOMMENDED PROJECTS

Springdale Northern Bypass BENTON & WASHINGTON COUNTIES

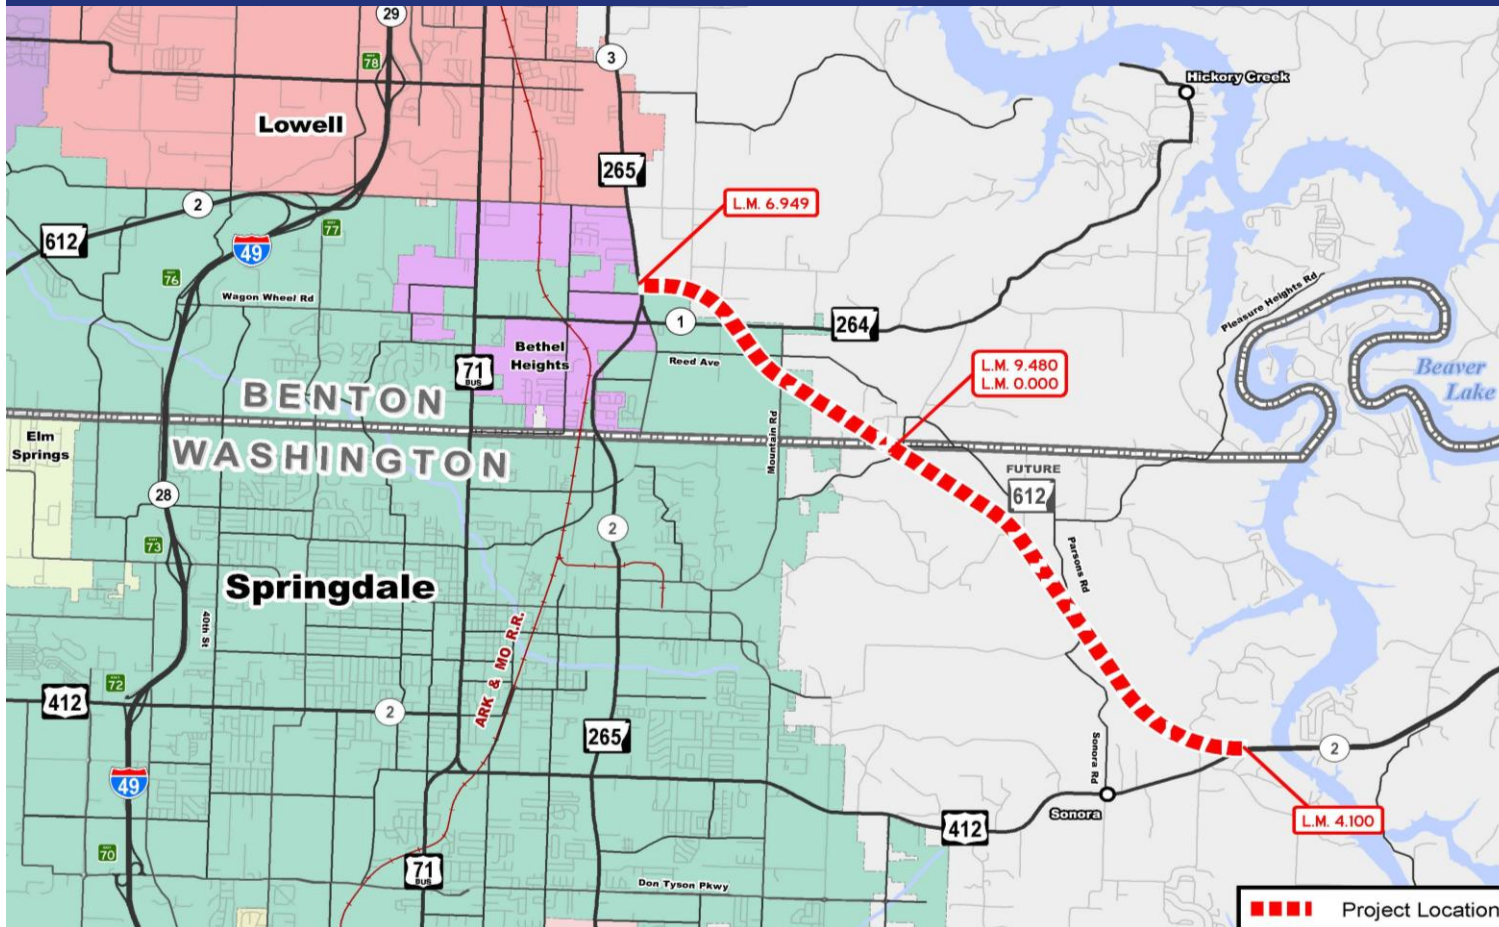

Highways 7, 22, & 27 YELL COUNTY

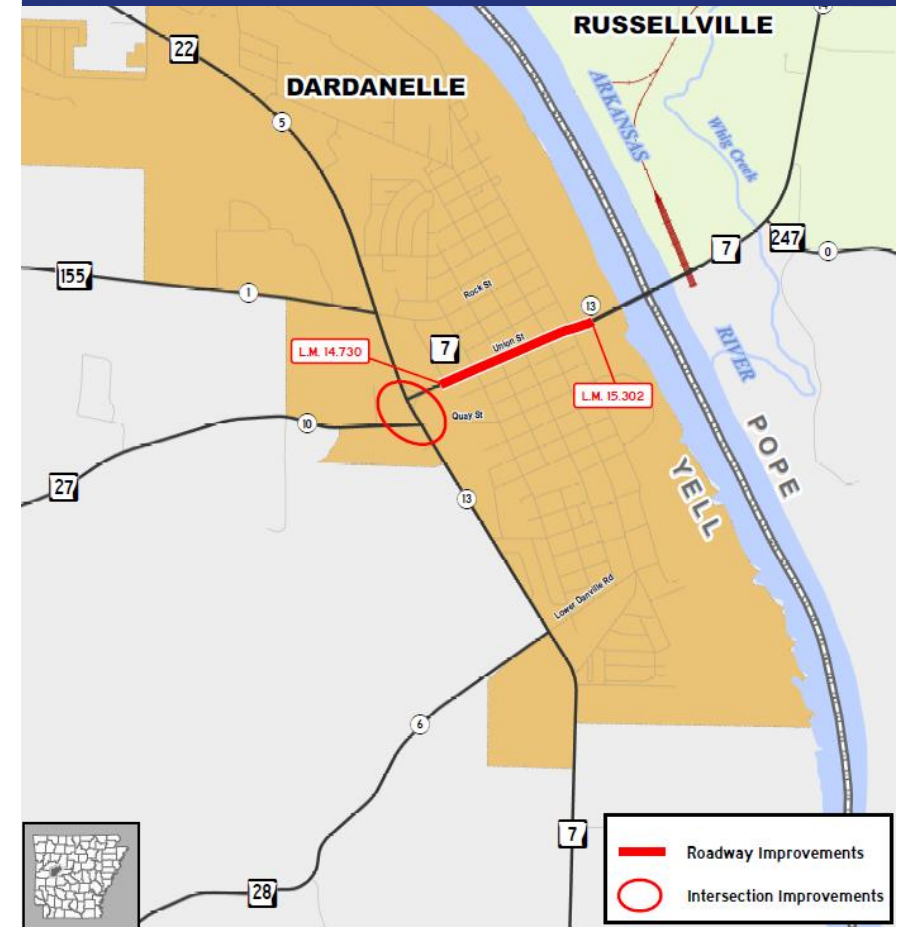



2024 Fall Equipment Auction

PROCEED REPORT

Units/Lots Sold	
Equipment Units	116
Equipment Implements	23
Miscellaneous Minor Equipment Lots	84
Lots of Miscellaneous Items	111
Total	334

Auction Proceeds	
Gross Proceeds	\$850,351.00
Auctioneer's Commission (6%)	(\$51,026.06)
Net Proceeds to the Department	\$799,329.94





Arkansas State Highway Commission Meeting

December 4, 2024
